

FROM (NAME & LOCATION) C. F. Buckley - WGK

DATE June 7, 1974

SUBJECT Status - PCB Environmental Control Program

REFERENCE

TO :

J. R. Savage - B2SL

CC G. L. Bratsch
W. C. Engman
M. R. Foresman
P. E. Heisler
G. A. Hippe
P. B. Hodges - E1SF
A. E. Leisy/G. Johnson
A. Gallion
W. B. Papageorge - B2SL
W. R. Richard - T3A

I. PCB Level In Sewers

May losses at 4.5 lb/day from operating departments and the incinerator compared to 1.0 lb/day of last month.

- A. Aroclor Department. PCB losses increased to 4.4 lb/day from 1.0 lb/day of last month.
- B. Incinerator losses remained low at 0.1 lb/day.
- C. Waste Treatment Influent. Losses averaged 4 lb/day compared to 5 lb/day of last month.
- D. Waste Treatment Effluent. Losses averaged 3 lb/day compared to 4 lb/day of last month.

II. Project Status

All projects are complete. The HCl Scrubber operated satisfactory throughout the month. Water consumption has been reduced and air blowing has been eliminated, however water recycle had to be cut back slightly to avoid excessive temperature. Some air is withdrawn from the vapor spaces of the intermediate storage tanks by the small drowning jet.

III. Program Status

The HCl pressure control valve opened 10 times for very short periods during the month.

Losses from the department were higher than normal. The source of this material was traced to the drowning jet which pulls air from the intermediate storage tanks and some entrained material was drained from the duct between the demister and the jet. The demister however appears to be in good shape. Losses have declined to 1 lb/day since the duct was drained, and the accumulation in the duct has not recurred.

DSW 353138

STLCOPCB4085329

III. Program Status (Cont'd)

Department 217 used the entire output of HCl from Dept. 246 but negligible amounts of PCB appeared in the sewer which receives the waste liquor from the C/S scrubber. This suggests that the amount of PCB in the HCl gas has been reduced by the new (Aroclor) scrubber to a level which is well within the capacity of the C/S scrubber.

No PCB was found in the Department 236 sewer. This indicates that the pressure control system effectively prevents the passage of HCl from Dept. 246 to the 236 area where it could be sewerred.

The above results from 217 and 236 were confirmed by samples obtained further downstream (sewer box 3E) which consistantly analyzed below 10 ppb.

IV. Future Plans

Projects are being developed to upgrade the curbing around the incinerator area and to provide flow measurement and proportional sampling of the waste water. Estimates are nearing completion.


C. F. Buckley

C. F. Buckley


dy

WASTE TREATMENT PLANT

#/day

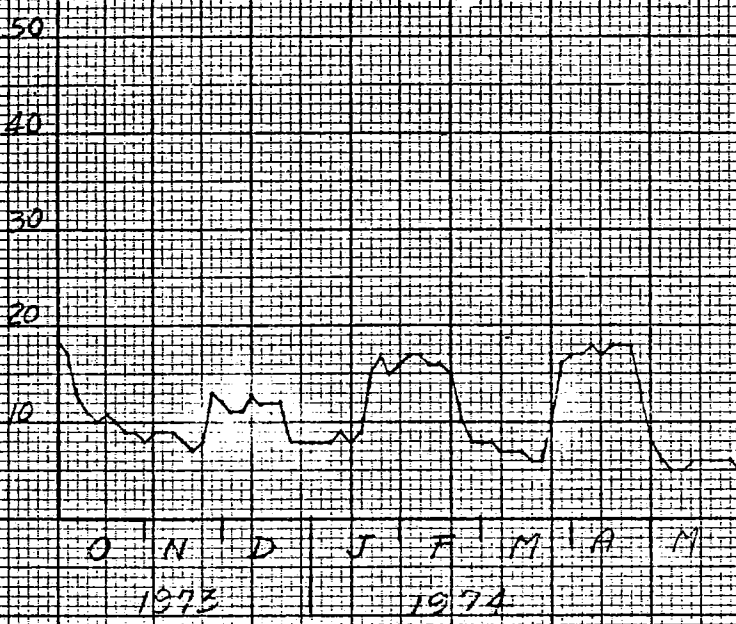

INFLUENT

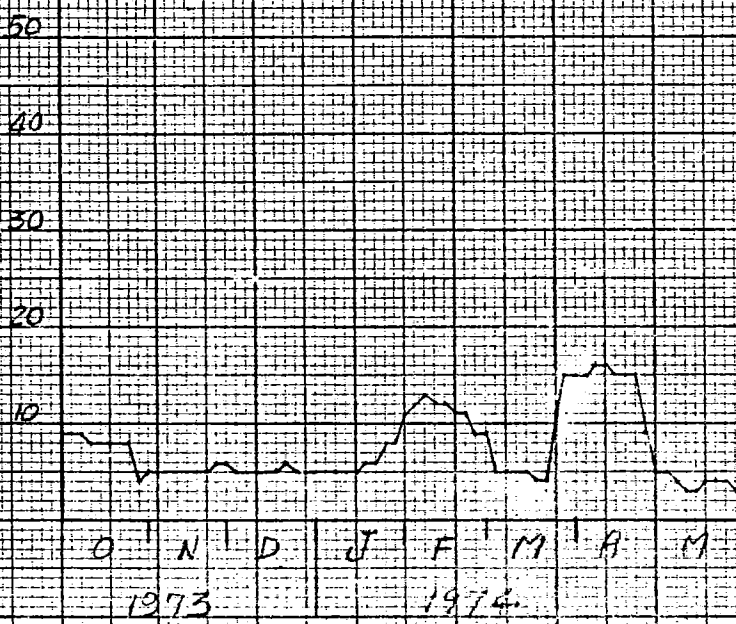

EFFLUENT

Each point represents average of past 31 days
