


PLAINTIFF'S EXHIBIT

SH-1752

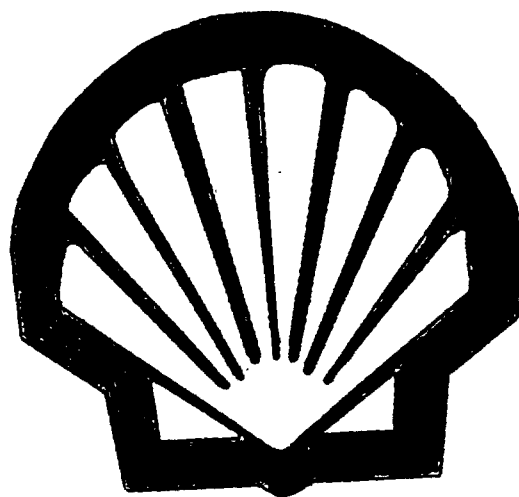

SHUTDOWN
AND
DECONTAMINATION

A / G DEPARTMENT
1991 SHUTDOWN

LAM 018166

DPMC-11838

05/09/91 Thursday
9:36 am

IPA-TURNAROUND MAY 1991
Filename: IPA-MAY-91

Page 35

EQUIPMENT : PP-40	PP-40: REMOVE INSULATION ON 50# STEAM	Area: ADIS
W.O. # : 031685	LINE AND CHANGE OUT GASKETS.	E.C.: PP
DAYS/HRS : 6x20	LOC: WEST OF V-25 IN RACK UNDER PUMP	W.C.:
HRS/SHIFT : 10	SHED ROOF	
UNIT CODE :		

JOB NO.	I	J	DESCRIPTION	REQUIRED M-H	CRAFT	CREW	SCHEDULED FROM	TO
203.	1	5	PP-40: BUILD A SCAFFOLD FOR ACCESS TO FLANGES	9	CARP	3	Not Sched	
204.	5	10	PP-40: REMOVE ASBESTOS INSULATION ON STEAM LINE AT FLANGES (LINE MUST BE SHUT DOWN TO REMOVE ASBESTOS INSULATION)	16	INSL	3	1/1	1/1
205.	10	15	PP-40: OPEN FLANGES AND INSPECT FOR CUTS ON GASKET SURFACE. THEN REPLACE GASKET AND MAKE UP FLANGES	4	PF	2	2/1	2/1
Early Restraint: 2/ 1								
206.	15	20	PP-40: HAVE OPERATIONS ENERGIZE STEAM LINE & INSPECT FOR LEAKS. IF NO LEAKS ARE FOUND; HAVE OPERATIONS KILL THE STEAM TO INSULATE LINE	1	OPER	1	2/1	2/1
				1	PF	1		
207.	20	25	PP-40: INSULATE FLANGES	16	INSL	2	2/1	2/2
			Late Restraint: 4/20					
208.	25	30	PP-40: REMOVE SCAFFOLD POST	9	CARP	3	Not Sched	

Resource Manhours :

1 OPER : 18 CARP : 32 INSL : 5 PF :

LAM 018167

DPMC-11839

A / G DEPARTMENT
1991 SHUTDOWN
SHUTDOWN AND DECONTAMINATION

A DISTILLATION

- 11] PULLING THE NORTH STEAM CONTROL VALVE ON C-3102 AND
SENDING IT TO SHOP, FV-5062.
- 12] INSTALLING PIPING AND VALVES FOR BACK WASHING C-3102
CONDENSERS.
- 13] REPLACING THE VALVE AT C-9 WATER REFLUX LINE BACK TO C-9.
IT HAS BUSTED PACKING GLAND BOLTS. FEP VALVE #1349.
- 14] MAINTENANCE WILL BE REMOVING THE ASBESTOS INSULATION ON
THE 50 LB STEAM LINE WEST OF V-25.

LAM 018168

DPMC-11840

SHUT DOWN & DECONTAMINATION
A/G DEFARMENT
1991 SHUT DOWN

LAM 018165
