

CG 03 CODE KY-787-D PKG PROCESSES APPROVED BY
 LOT DATE DEC-16 80 38252 () KY-787-D (R) FWP 12/04/80
 TIME () XOB-17: 25% LESS SILICA &
 EST'D WGT 932 LBS () A 240 MIN STRIKE
 STANDARD HRS. 8.9

COMTYP JOB NAME: XOB17:787Q

COMPONENT CONSUMPTION									
CG	CODE	LOT	PQ	LBS	CG	CODE	LOT	PQ	LBS
14	YC002B		93		14	YC002B		93	
14	YC002B		93		14	YC002B		93	
14	YC002B		93		14	YC002B		93	

Note STEP 27

Homog # 3 - 22d Pass

TOTAL EST'D WGT 3332

NON-BLEEDING

DEC 18 1980

EQUIP	NAME : "KROLOR" YELLOW-MEDIUM	USE LBS	N- CODE	ACCT LBS
203	1 RUN 60" (990 G) WATER IN V-203. SET AGITATOR ON HIGH SPEED.			
205	2 WEIGH IN DRUM & POUR IN	245	983-D	245
	3 DUMP IN AND STIR 5 MIN	48X50	YC-2-B	2400
	RECORD: START <u>1:20 PM</u> LOT <u>13410</u> 47x50			
	FIN <u>1:20 PM</u> <u>13371</u> 1x50			
	4 ADJUST TO 75" (1275 G)			
	5 WITH AGITATOR ON LOW SPEED PUMP V-203 THRU HOMOG AT 2400-2600 PSI INTO V-205			
	6 WHEN V-203 MT, WASH COLOR THRU HOMOG WITH MIN OF HOT WATER AT 2400-2600 PSI INTO V-205			
	7 RECORD: V-205 VOL <u>56</u> " & ADJ TO 60" (2100 G)			
	8 INSPECT HOMOG STRAINER & CLEAN IF NECESSARY			
205	9 RUN 10" (514 G) WATER INTO V-243 & START AGITATOR			
SV	10 PUMP V-205 THRU HOMOG AT 4800-5200 PSI INTO SV.			
	RECORD: TIME START <u>12:10</u> TOTAL MINUTES <u>110</u>			
2	NOTE: IF HOMOG PRESSURE FALLS BELOW 4800 PSI, 3-WAY VALVE WILL RECIRCULATE SLURRY TO V-205			
	11 WHEN V-205 MT, RUN IN 5" (240 G) WATER & PUMP THRU HOMOG AT 4800-5200 PSI INTO SV			
SP	12 SP STEP 01 - SET FORMULA SELECTOR TO POSITION 2 (V-243) OR POSITION 7 (V-244)			
CP	13 PRESS SV CAM RESET PB - SET 22 TC IN AUTO			
	REMOTE (TEMP IS SET AT 190-194°F)			
3	14 RECORD LEVELS & SET R/M COUNTER #1 AS FOLLOWS:			
	A. 11LG 22% PRESET #1 80 GAL 15-A 160			
	B. 13LG 56% PRESET #6 135 GAL 20-A 135			
15	SET STRIKE FLOW CONTROLLERS AS FOLLOWS:			
	3FC10 (N-27-D CONTROLLER) IN MANUAL 0.39 GPM 27-D 206			
	3FC20 (N-27-D WATER) IN MANUAL LOCAL 5.28 GPM			
	3FR10 (N-27-D/WATER) RATIO 1.35			
	3FC10 (N-32-D CONTROLLER) IN MANUAL 0.50 GPM 983-D 1405			
	3FC20 (N-32-D WATER) IN MANUAL LOCAL 4.55 GPM			
	3FR20 (N-32-D WATER) IN REMOTE			
	3FR10 (N-32-D/WATER) RATIO 1.82			

PUNCHED & CHECKED

DEC 18 1980

V-243

118 OPERATOR STEP PB
 320 117 RECORD LEVEL 2LG 52% IF BELOW 35% FOLLOW SOL 'N'
 SV MAKE-UP PROCEDURE FOR N-27-D
 SP 118 ADJUST SV TO 48" (2470 G)
 CP 119 RECORD PH 10.3 ADJ TO 11.1-11.3 WITH N-7-D AT
 5% (10 PARTS WATER TO 1 PART N-7-D)
 4 120 SIPHON INTO SV. RECORD: PH 11.1 ASSUME 50% 24 7-D 12
 120 OPERATOR STEP PB

121 SP STEP 06/39. AFTER HEAT-UP RECORD: PH 9.75
 SV 122 SWITCH 3FC20, 8FC10, & 8FC20 TO AUTO
 SP 123 OPERATOR STEP PB
 124 SP STEP 10/43. WHEN 3FC20, 8FC10 & 8FC20 FLOWS
 ARE IN LIMITS, SWITCH 3FC10 TO AUTO & PB
 5 125 SP STEP 11/44. WHEN 3FC10 & 3FC20 FLOWS ARE IN
 LIMITS, SWITCH 3FC20 TO REMOTE
 126 OPERATOR STEP PB
 127 DURING STRIKE RECORD:

SP STEP

V-243/V-244

13/46 (30 MIN)

14/47 (60 MIN)

15/48 (2 HRS)

16/49 (3 HRS)

16/49 (4 HRS)

17/50 (FINISH)

PH RANGE TIME

8.6 9.0-10.0 4:15

9.2 9.0-10.0 4:45

9.35 9.0-10.0 5:45

9.4 9.0-10.0 6:45

9.4 9.0-10.0 7:45

6.9 7.5-8.5 8:30

NOTE: IF PH NOT IN RANGE, NOTIFY SUPV & NOTE
 IN LOG. IF FINAL PH > 8.5, ADJ TO 7.5-8.5.

& RECORD: PH ____

ASSUME 77%

27-D

3:45/AM

Shot N-27 Down
 5 min increased
 N-32
 Sounds Like Air
 Leaking

128 WHILE STRIKING RUN 30" (234 G) WATER INTO V-339
 129 ADD IN 7-8 MIN 350 530-A 350
 339 130 ADJ TO 49" (382 G) AT 80-100*F
 6 131 STIR 5 MIN & RECORD: PH 11.2 (9.5-10.5)
 132 STIR 15 MIN OR LONGER FOR SP STEP 26
 133 RECORD: VOL 49 & CALC 49 X 0.78 = 38.2 GAL
 134 SET PRESET #8 TO 38.2 GAL FROM S 33

302 135 RUN 30" (380 G) WATER INTO V-302
 7 136 ADD & STIR 2 MIN FOR S 40 ASSUME 50% 160 7-D 80

137 SP STEP 17/50 AFTER CHECKING PH, OPERATOR PB.
 138 SIFT IN 100 128-A 100
 SV 139 SP STEP 23/53. RECORD: PH 3.8 (3.7-4.2)
 SP 140 RUN IN N-7-D FROM S 36 IN 10-12 MIN & STIR 5
 MIN
 8 141 RECORD: PH 10.2 (9.0-9.5). ADJ IF NECESSARY &
 RECORD: PH 9.2 ASSUME 77% 15 27-D 12
 (DILUTE 10 PARTS WATER TO 1 PART) ASSUME 50% 7-D
 (SIPHON N-7-D INTO SV)
 142 OPERATOR STEP PB
 143 SP STEP 29/58. RECORD: PH 9.0 & TIME ____
 144 OPERATOR STEP PB
 145 SP STEP 60. BATCH COMPLETE.

START
TIME SP STEP

7:00 P

7:00 P

7:00 P

FINISH

TIME SP STEP

3:00 P

7:00 A


10:00 A


OPTR


223-282


235-

282

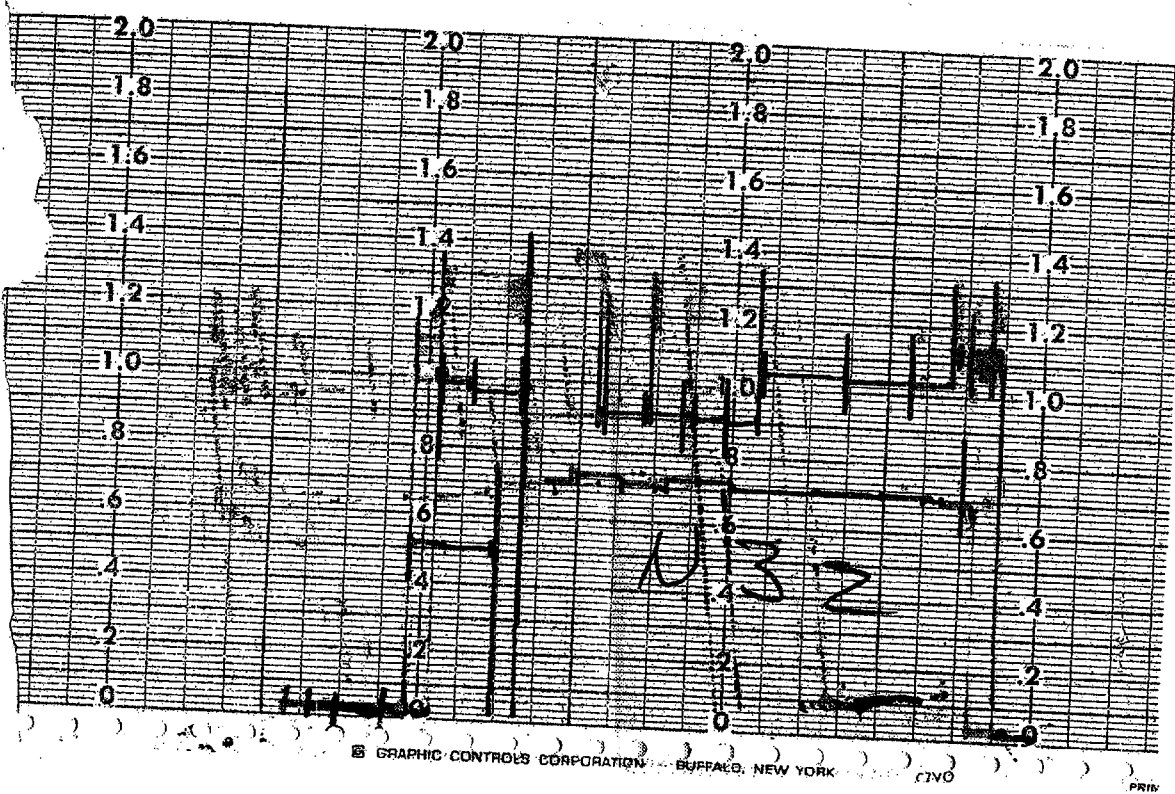

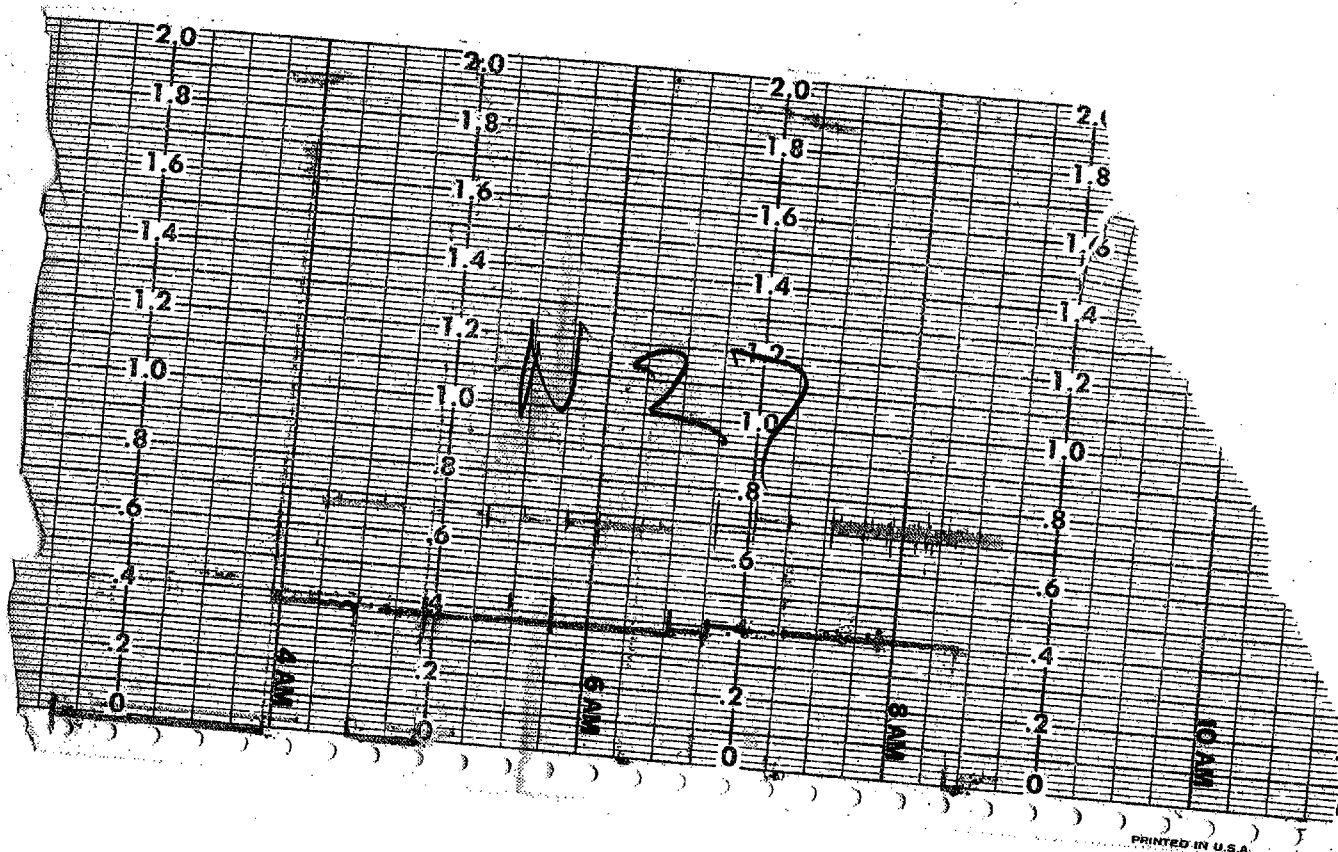

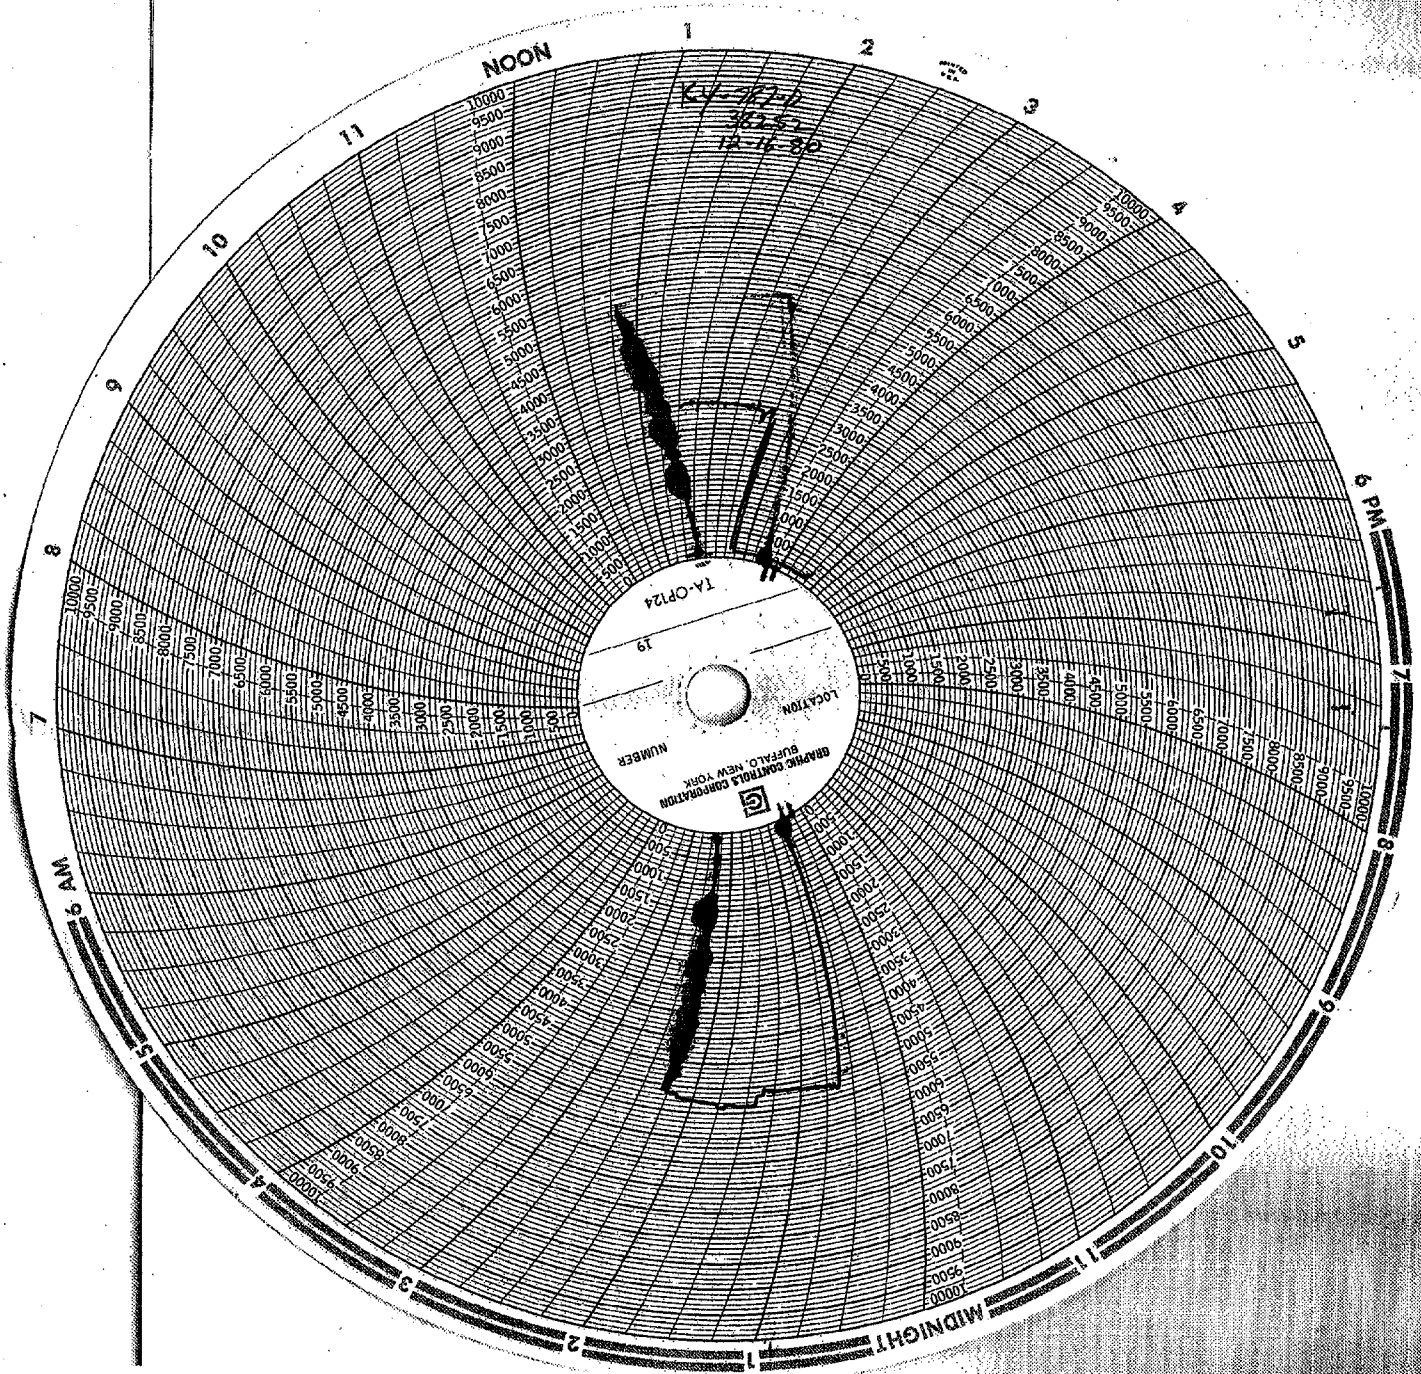

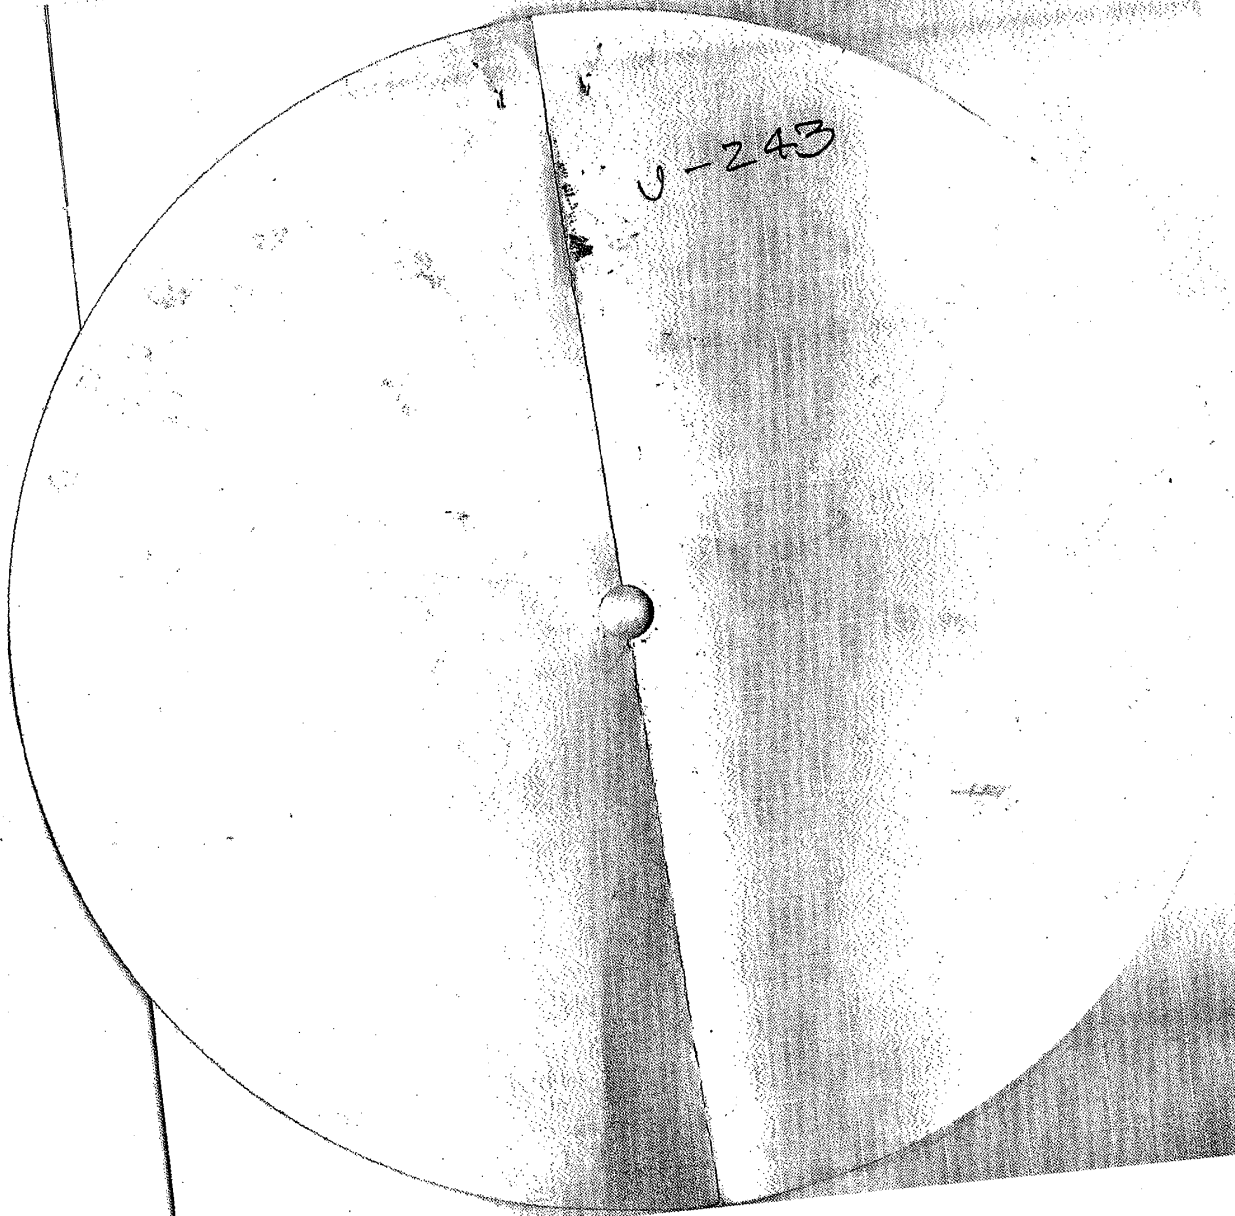

DUP050105089
