MAKING INSTRUCTIONS: BATCH UNIT

C.V. 260

D.V. 303, 315, 317, 322, 323

40 CODE RT-531-D PKG.

DEC -1 80 38084

T. WGT. 665 LBS.

TD. HRS. TIME 3P M

PROCESSES		APPROVED BY
(P)	RT-531-D (N)	BBK 04-25-77
(C)	RT-160-P ( )	DCG 04-26-77
( )	( )	MTW 04-27-77
( )	( )	
TYPED BY emw042977		

RUN N-3-A SOLN THRU WEST PRESS

NON-BLEEDING

ENT		NAME: NAPHTHANIL® RED LIGHT	USE LBS.	N CODE	ACCT. LBS.
ep	1	Obtain for S 6		504-C	
1	2	Obtain for S 18		150-C	
	3	Clean, dress, close 24" clarif press - 15 frames			
NOTE		CLEAN WEST PRESS - LINES + ETC	40	3	40
	4	Run 20" (486 G) water into V-303			
2	5	Run in from V-324 M11 , 30.87 %	408	28-D	126
	6	Dump in from S 1 Lot		504-C	~~240~~
		5055	211		211
	7	Add & stir 15 min to wet Lot	~~1~~	~~396-C~~	~~1~~
	8	Adj to 43" (1020 G) at 40-45°F	3x 330	57-A	990
	9	Pour in AFAP M 13 , 33.47 %	284	725-A	95
	10	Stir 5 min & Record: CR + (+) M , %		28-D	
		KI + (+), Temp 42 (40-45°F) M , %		725-A	
	11	Stir 10 min at 40-45°F maintaining + CR & + KI for S 13		57-A	
		Record: Start 5:10 PM CR + (+), KI + (+)		725-A	
C	12	Slurry in 40 Gal water in drum & precoat clarif press	5	777-A	5
3					
	13	When S 11 stir complete, dump in	15	113-A	15
4	14	Dump in	10	777-A	10
	15	Stir 30 min at 40-45°F maintaining + KI for S 23		725-A	
		Record: Start 5:20 KI + (+)		57-A	
D	16	Run 13" (177 G) water into V-330			16
5	17	Slurry in 25 G water & pour in	16 24	39-A	~~24~~
	18	Dump in from S 2 & stir 30 min or longer to wet Lot		150-C	370
		Record: Start 6:45 PM 70457	130		
		70593	65		
		70457	65		
		70456	65		
		70584	45		
	19	Run 12" (144 G) water into V-302 314			
V-346	20	Pour in Assume 50%	29 ~~58~~	721-D	29
	21	Siphon in & stir 3 min M 11 , 76.63 %	86	30-D	43
	22	Record: pH 1.4 (6.7-7.5) Assume 50%		7-D	
		If necessary adj to 6.7-7.5, Record: pH Assume 75%		30-D	

MTW

PRINT		PAGE 2 CG 40 CODE RT-531-D (N) EST. WGT. 665 LBS.	USE LBS.	N CODE	ACCT LBS.
7	23	Pump DV thru clarif press into V-323 maintaining temp at 40-45°F. Record: Start 5:55 P.M Total Min 30	2 x 330	57-A	660
		NOTE: Do not use V-303 - too small			
	24	When S 23 clarif complete, wash DV (S 4) lines, pump & press for 20 min or to a -CR test on a sample of total press effluent, whichever comes first. Collect washings in DV (S 23) Record: Start 6:25 P CR — (- or +)			
	25	When S 24 is complete, test DV (S 23) & Record: KI + (+), Temp 41 (40-45°F)		725-A 57-A	
	26	Weigh in Rubber Bucket & Rinse in & stir 3 min	10	395-D	10
	27	Record: KI —. Must be - & If necessary adj to - KI	~~2~~	395-D	~~2~~
	28	Adj to 56" (1925 G) at 40-45°F	~~1 x 330~~	57-A	~~660~~
		39"			
0 8	29	Run 23" (3900 G) water into V-260			
	30	Install Temp Chart & Set Agitator at 16 RPM			
30 9	31	When S 18 stir complete pour in, in 3-4 min Assume 50%	110 220	72.1-D	110
	32	Heat to 128-132°F AFAP & stir 5 min to dissolve. Stop agitator			
0 10	33	Immediately run V-330 AFAP into CV. No agitation in CV Record: Start 9:45 P Total Min 8			
	34	Pour in & stir 5 min M 11 , 76.63 %	196	30-D	150
	35	Record: pH 10.9 (10.5-11.0) Assume 50%		7-D	
		If necessary adj to pH 10.5-11.0 Record: pH ~~—~~ Assume 75%		30-D	
	36	Run in V-302 AFAP			
	37	Pump in	35	65-A	35
	38	Heat to 78-82°F & Record: HT 79 °F & Rec 82 °F			
	39	When S 28 complete, couple DV undersurface in 65-70 min Maintain CV at 78-82°F Record: Start 11:00 Total Min 75			
	40	Record: Diazo ~~—~~ (- or +) Base + Must be + pH 4.5 (4.2-4.6)			
	41	If necessary stir to - diazo Record: Start 12:35 Total Min 20 Record: Diazo — Must be - Base + Must be + pH 4.5 (4.2-4.6)			
SC 11	42	Dissolve in 30 G water at 130-140°F in drum for S 43	30	567-B	30
0 12	43	Pour in N-567-B sol'n from S 42			
	44	Heat to 194-196°F in 55-60 min & Record: HT 196 °F & Rec 198 °F			
SC 13	45	Dissolve in 35 G water at 140-150°F in drum for S 46	60	15-A	60
0 14	46	When S 44 heating complete, pour in N-15-A sol'n from S 45 into CV			
	47	Stir 30 min at 194-196°F			
	48	Flood to ~~62" (4150 G)~~ 80" (7928 G) & stop agitator			

VAT	V-303	V-315	V-317	V-322	V-323
S 4 (486 G)	20"	14"	14"	14"	14"
S 8 (1020 G)	43"	30"	30"	30"	30"

START 3:00 P.M FIN 2:55 A.M OPTR 381

Meeting - 30 minutes

DUP050106857

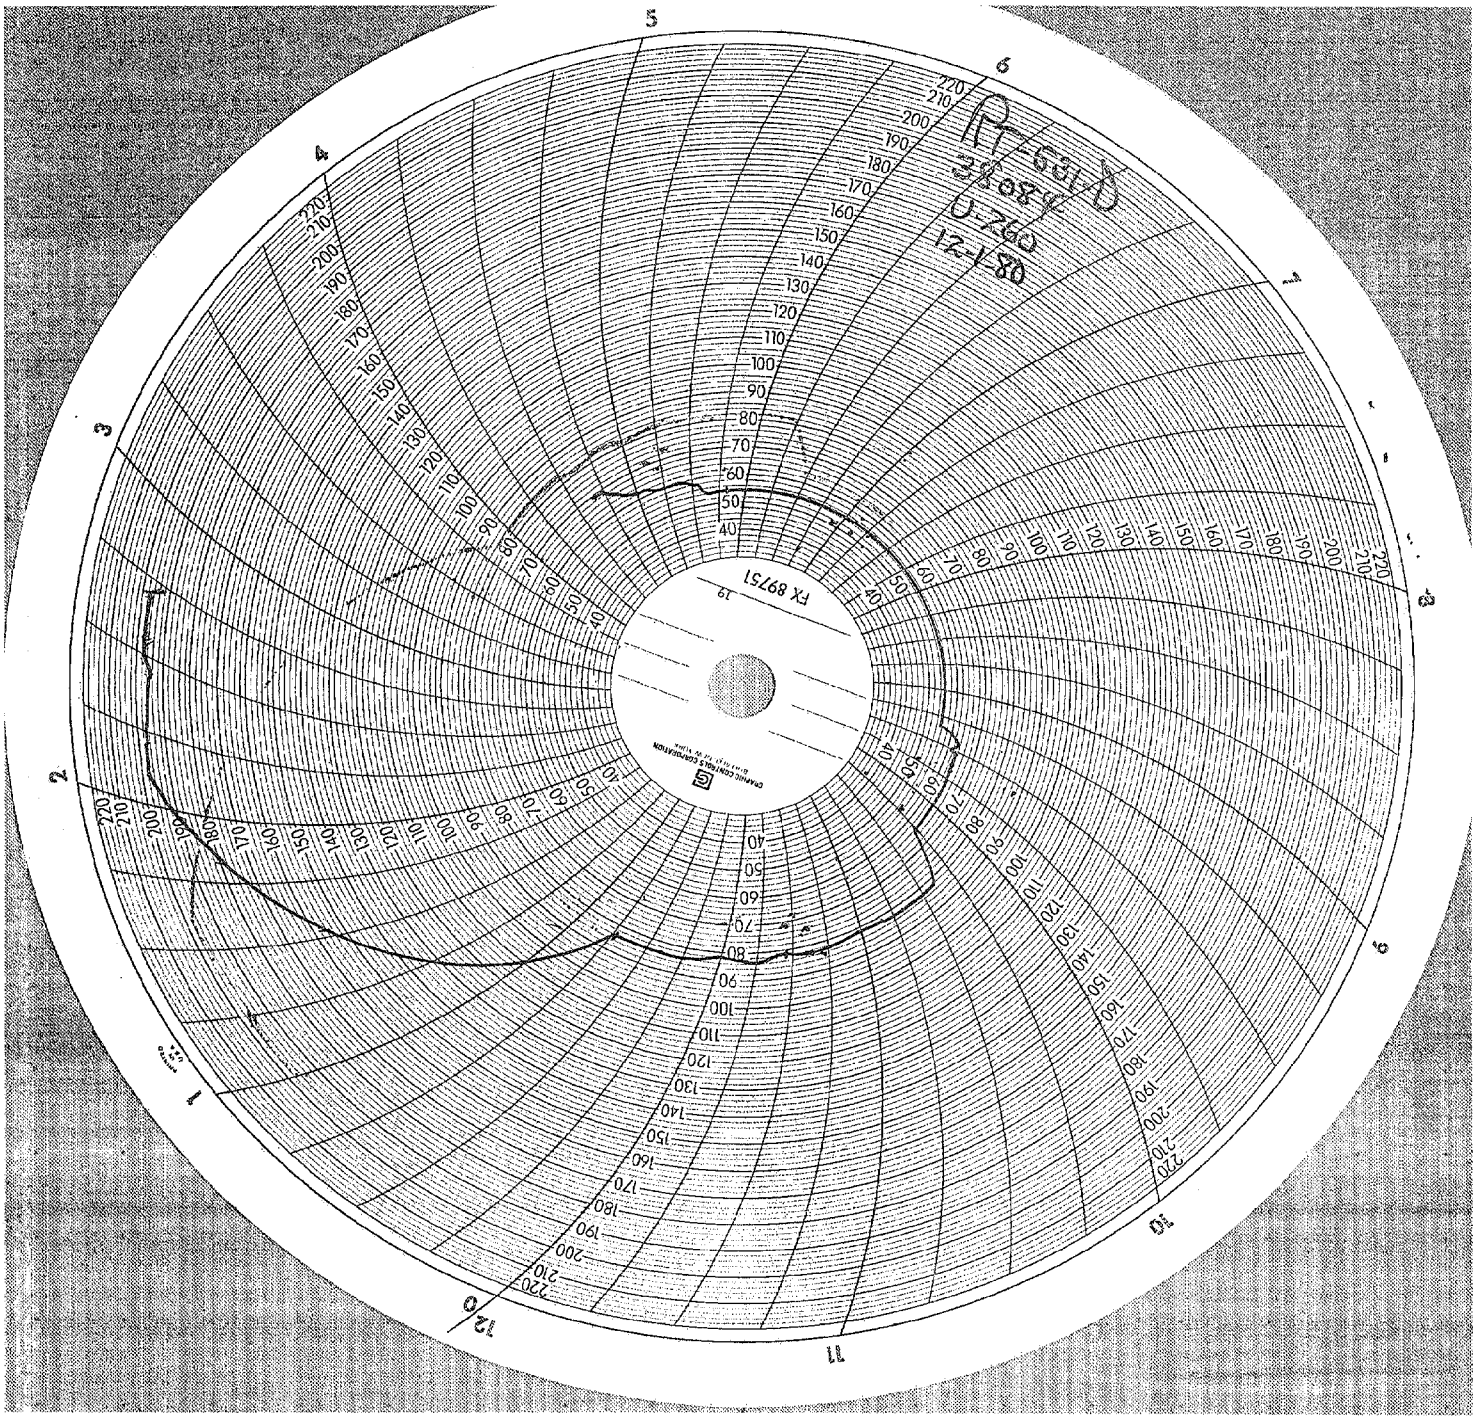

DUP050106858
