COMPANY CONFIDENTIAL

Monsanto

FROM (NAME & LOCATION): C.F. Buckley - WGK

DATE: June 7, 1973

SUBJECT: Status - PCB Environmental Control Program

REFERENCE:

TO: J.R. Savage - B2SL

cc: G.L. Bratsch
W.C. Engman
M.R. Foresman
P.E. Heisler
G.A. Hippe
P.B. Hodges
A.E. Leisy/J. Grant
D.C. Otto
W.R. Richard - T3A

I. PCB Level in Sewers

May losses at 1.15 #/day from operating departments and the incinerator are 30% higher than last month.

A. Aroclor department. PCB losses from the department increased to 1.10 #/day from .77 #/day. High losses were recorded due to HCl sewering when the chlorine emission of May 22, 1973 disturbed operations at chlorine using departments.

B. Incinerator losses decreased to 0.06 #/day from .11 #/day of last month. The incinerator was partially down during the month.

C. Waste Treatment Influent. Losses averaged 4.7 #/day compared with 7.5 #/day of last month.

D. Waste Treatment Effluent. The level of losses were lower than last month at 4.7 #/day compared with 5.9 #/day of last month.

II. Project Status

Project 3956 "Alterations to HCl Distribution System" EDC now July 1, 1973.

Project 4438 "Reduce Water Flow to Sewer" Construction scheduled for next month.

Project 8020 "HCl off Gas Scrubber". No EDC as yet for installation.

III. Program Status

1. HCl Off-Gas. The sewering valve opened several times due to over pressure when the c/s department was down due to the chlorine emission of May 22.

DSW 353174

2. Blow Tank Off-Gas. No change pending completion of project 4438.


3. Rip Track Washes. 17 cars were washed during the month and the accumulation of the settling tank increased to 3260 gallons. The overflow of the tank will be measured to find out if the losses are still under control.

C.F. Buckley

J.A. Munoz

dm

DSW 353175

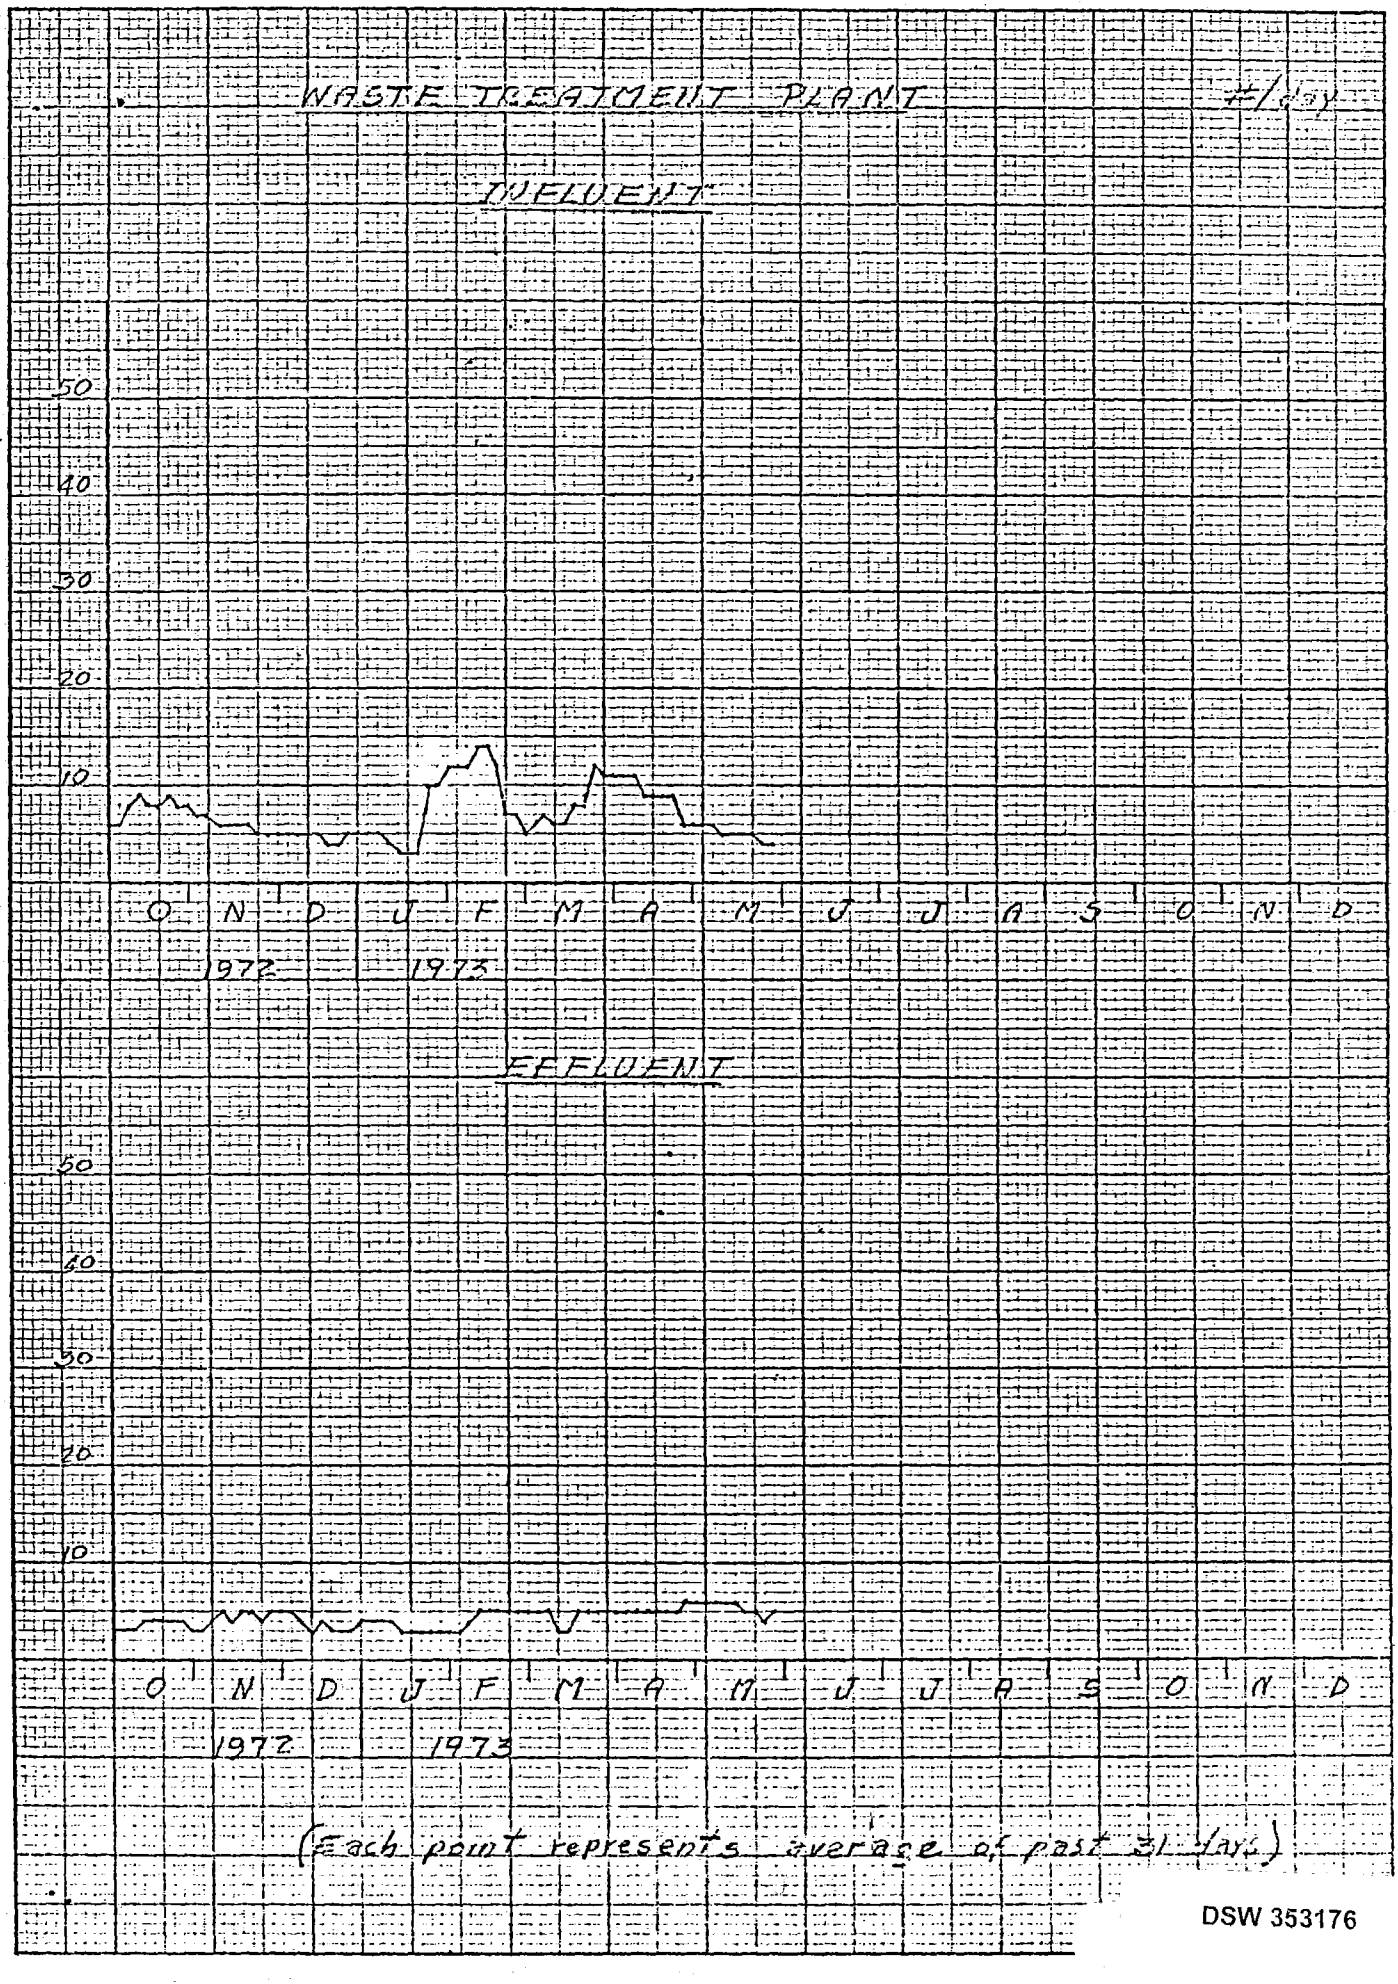

K&E 10 X 10 TO ½ INCH 46 1320
7 X 10 INCHES MADE IN U.S.A.
KEUFFEL & ESSER CO.

DSW 353176

STLCOPCB4085367
