CG 63 CODE KY-787-D PKG

LOT OCT--0830 37351

EST'D WGT 932 LBS

STANDARD HRS. 8.9 TIME 11AM 11PM

PROCESSES
( ) KY-787-D
( )
( )
( )
( )

APPROVED BY
(Q) FWP 9/23/80
( ) (XOB-17: 25%
( ) LESS N-32-D
( ) & 240 MIN
( ) STRIKE)

TYPED BY: FP 9/23/80

COMPONENT CONSUMPTION

CG	CODE	LOT	PQ	LBS
14	YC002B	13088	93	2000
14	YC002B	13096	93	400
14	YC002B		93	

CG	CODE	LOT	PQ	LBS
14	YC002B		93	
14	YC002B		93	
14	YC002B		93	

TOTAL EST'D WGT 3332 NON-BLEEDING

EQUIP		NAME : "KROLOR" YELLOW-MEDIUM	USE LBS	N-CODE	ACCT LBS
203 & 205	1	RUN 60"(990 G) WATER IN V-203. SET AGITATOR ON HIGH SPEED.			
	2	WEIGH IN DRUM & POUR IN	240	32-D	240
	3	DUMP IN AND STIR 5 MIN LOT	48X50	YC-2-B	2400
		RECORD: START 5:30 AM 13088 2000	2000		
1		FIN 6:40 AM 13096 400	400		
	4	ADJUST TO 75" (1275 G)			
	5	WITH AGITATOR ON LOW SPEED PUMP V-203 THRU HOMOG AT 2400-2600 PSI INTO V-205			
	6	WHEN V-203 MT, WASH COLOR THRU HOMOG WITH MIN OF HOT WATER AT 2400-2600 PSI INTO V-205			
	7	RECORD: V-205 VOL 50 " & ADJ TO 60" (2100 G)			
	8	INSPECT HOMOG STRAINER & CLEAN IF NECESSARY			
205	9	RUN 10" (514 G) WATER INTO V-203 & START AGITATOR			
SV	10	PUMP V-205 THRU HOMOG AT 4800-5200 PSI INTO SV.			
		RECORD: TIME START 3:30 PM TOTAL MINUTES 120			
2		NOTE: IF HOMOG PRESSURE FALLS BELOW 4800 PSI, 3-WAY VALVE WILL RECIRCULATE SLURRY TO V-205			
	11	WHEN V-205 MT, RUN IN 5" (240 G) WATER & PUMP THRU HOMOG AT 4800-5200 PSI INTO SV			
SP & CP	12	SP STEP 01 - SET FORMULA SELECTOR TO POSITION 2 (V-243) OR POSITION 7 (V-244)			
	13	PRESS SV CAM RESET PB - SET 22 TC IN AUTO REMOTE (TEMP IS SET AT 190-194*F)			
3	14	RECORD LEVELS & SET R/M COUNTER #1 AS FOLLOWS:			
		A. 11LG 8.0% PRESET #1 80 GAL		15-A	160
		B. 13LG 5.2% PRESET #6 135 GAL		20-A	135
	15	SET STRIKE FLOW CONTROLLERS AS FOLLOWS:			
		SFC10 (N-27-D CONTROLLER) IN MANUAL 0.39 GPM		27-D	206
		SFC20 (N-27-D WATER) IN MANUAL LOCAL 5.28 GPM			
		SFR10 (N-27-D/WATER) RATIO 1.35			
		SFC10 (N-32-D CONTROLLER) IN MANUAL 0.49 GPM		32-D	1376
		SFC20 (N-32-D WATER) IN MANUAL LOCAL 4.47 GPM			
		SFC20 (N-32-D WATER) IN REMOTE			
		SFR10 (N-32-D/WATER) RATIO 1.82			

N34945

EQUIP		PAGE 2 CG 03 KY-787-D EST WGT 3332# V-243	USE LBS	N= CODE	USE LBS
	16	OPERATOR STEP PB			
320	17	RECORD LEVEL 2LG 92% IF BELOW 35% FOLLOW SOL'N			
SV		MAKE-UP PROCEDURE FOR N-27-D			
SP	18	ADJUST SV TO 48" (2470 G)			
CP	19	RECORD PH 8.8 ADJ TO 11.1-11.3 WITH N-7-D AT 5% (10 PARTS WATER TO 1 PART N-7-D)			
4		SIPHON INTO SV. RECORD: PH 11.2 ASSUME 50%	40	7-D	20
	20	OPERATOR STEP PB			
	21	SP STEP 06/39. AFTER HEAT-UP RECORD: PH 10.0			
SV	22	SWITCH 3FC20, 8FC10, & 8FC20 TO AUTO			
SP	23	OPERATOR STEP PB			
	24	SP STEP 10/43. WHEN 3FC20, 8FC10 & 8FC20 FLOWS ARE IN LIMITS, SWITCH 3FC10 TO AUTO & PB			
5	25	SP STEP 11/44. WHEN 3FC10 & 3FC20 FLOWS ARE IN LIMITS, SWITCH 3FC20 TO REMOTE			
	26	OPERATOR STEP PB 8:45 PM			
	27	DURING STRIKE RECORD:			
		SP STEP			
		V-243/V-244 PH RANGE TIME			
		13/46 (30 MIN) 9.6 9.0-10.0 9:15 PM			
		14/47 (60 MIN) 9.5 9.0-10.0 9:45 PM			
		15/48 (2 HRS) 9.0 9.0-10.0 10:45 "			
		16/49 (3 HRS) 9.5 9.0-10.0 11:45 "			
		16/49 (4 HRS) 9.5 9.0-10.0 12:45 AM			
		17/50 (FINISH) 8.2 7.5-8.5 1:30 AM			
		NOTE: IF PH NOT IN RANGE, NOTIFY SUPV & NOTE IN LOG. IF FINAL PH >8.5, ADJ TO 7.5-8.5. & RECORD: PH ___. ASSUME 77%	____	27-D	____
	28	WHILE STRIKING RUN 30" (234 G) WATER INTO V-339			
	29	ADD IN 7-8 MIN	350	530-A	350
339	30	ADJ TO 49" (382 G) AT 80-100*F			
6	31	STIR 5 MIN & RECORD: PH 10.0 (9.5-10.5)			
	32	STIR 15 MIN OR LONGER FOR SP STEP 26			
	33	RECORD: VOL 49" & CALC 49" X 0.78 = 38.5GAL			
	34	SET PRESET #8 TO 38.5GAL FROM S 33			
302	35	RUN 30" (360 G) WATER INTO V-302			
7	36	ADD & STIR 2 MIN FOR S 40 ASSUME 50%	160	7-D	80
	37	SP STEP 17/50 AFTER CHECKING PH, OPERATOR PB.			
	38	SIFT IN	100	128-A	100
SV	39	SP STEP 23/53. RECORD: PH 4.0 (3.7-4.2)			
SP	40	RUN IN N-7-D FROM S 36 IN 10-12 MIN & STIR 5 MIN			
8	41	RECORD: PH 9.4 (9.0-9.5). ADJ IF NECESSARY &			
		RECORD: PH___ ASSUME 77%	___	27-D	___
		(DILUTE 10 PARTS WATER TO 1 PART) ASSUME 50%	____	7-D	___
		(SIPHON N-7-D INTO SV)			
	42	OPERATOR STEP PB			
	43	SP STEP 29/58. RECORD: PH 9.2 & TIME 3:10 AM			
	44	OPERATOR STEP PB			
	45	SP STEP 60. BATCH COMPLETE.			

START TIME	START SP STEP	FINISH TIME	FINISH SP STEP	OPTR
10:01	_____	3rd	_____	120-126
3:00 PM	_____	11:00 PM	_____	237-37
11:15	_____	3:10 AM	_____	223-381

PUMP TO VAT 240

DUP050105939

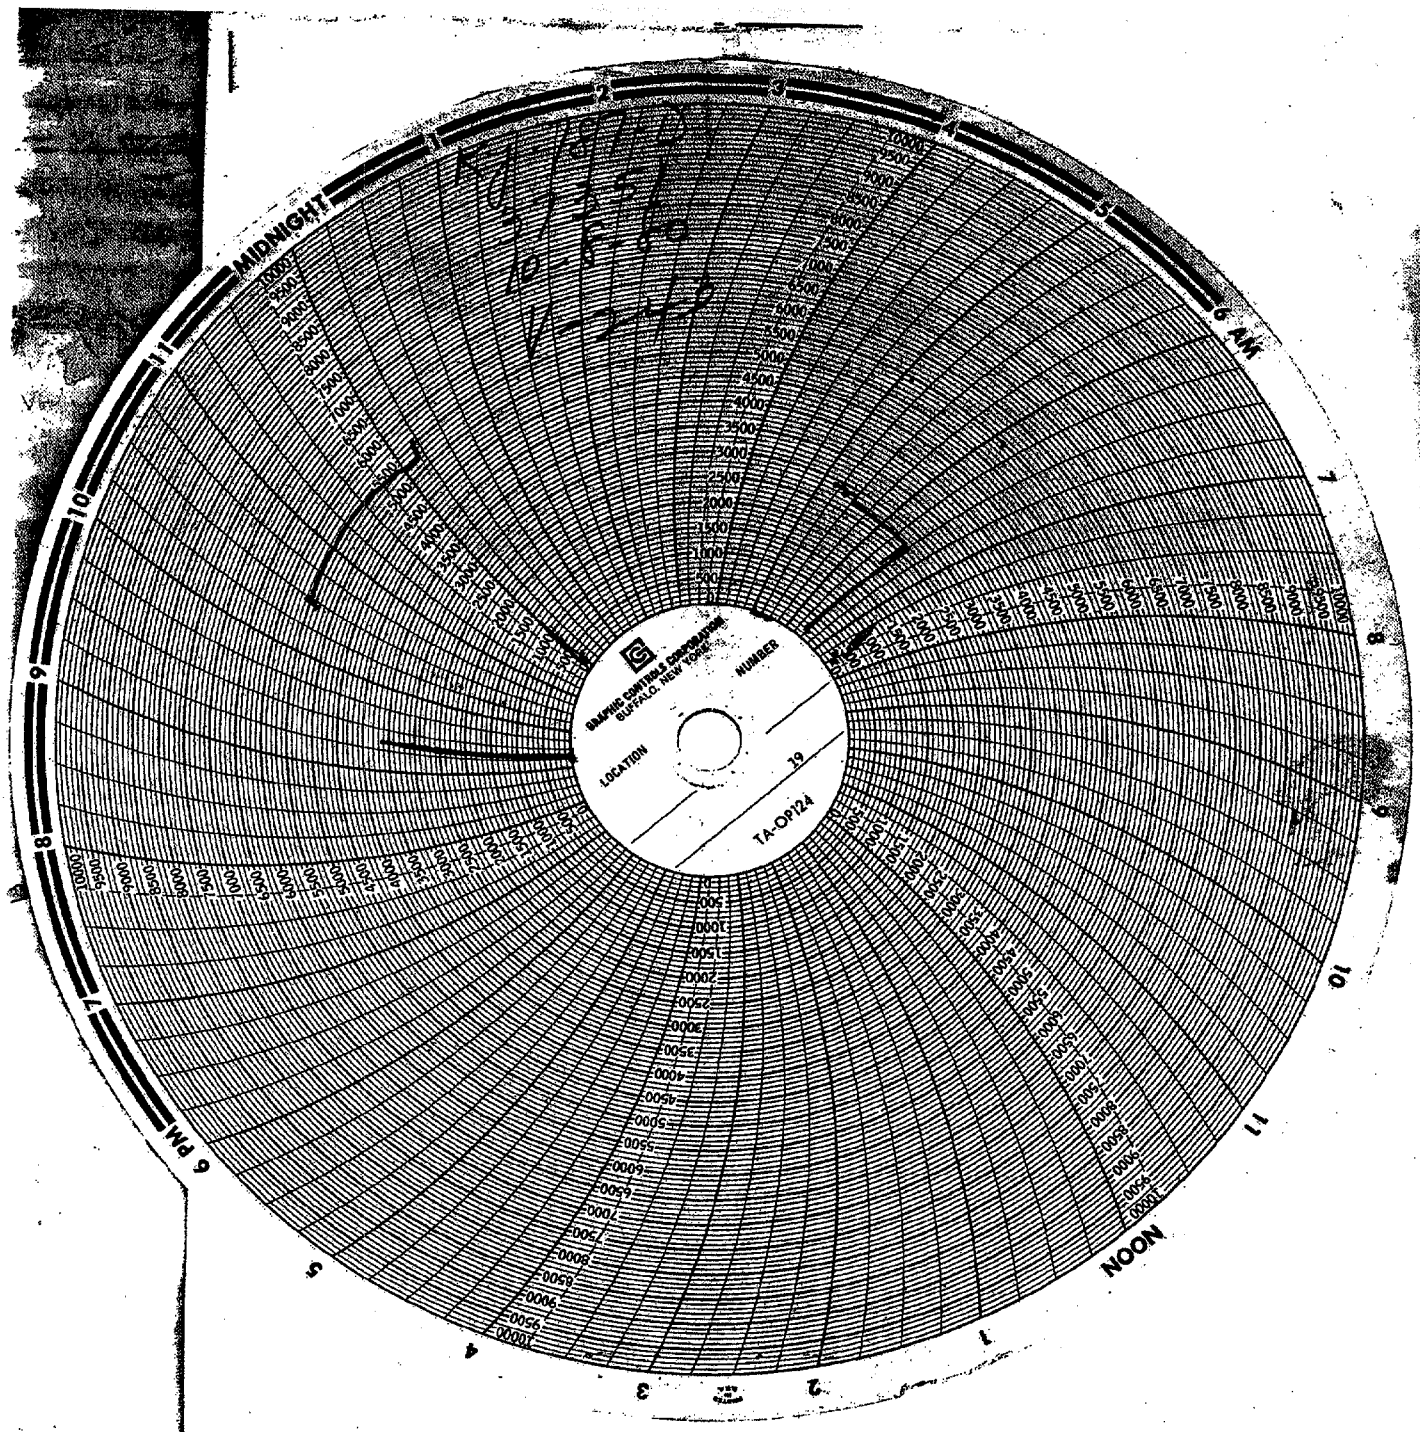

DUP050105940

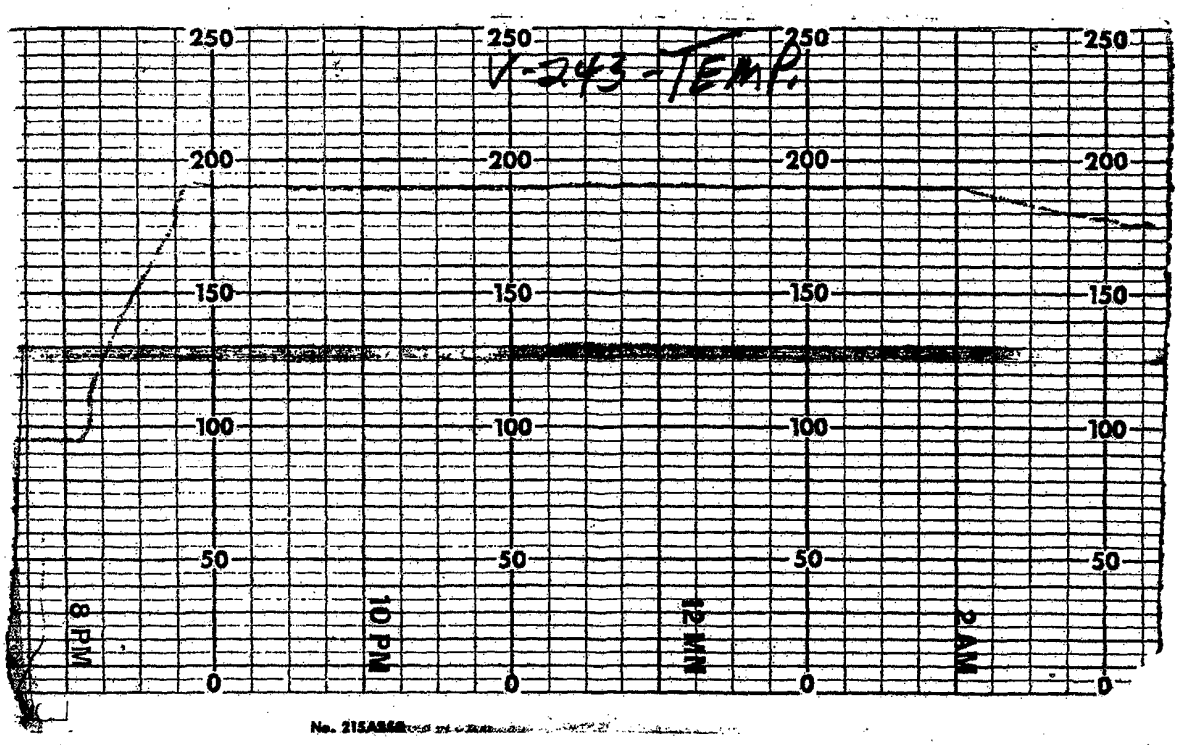
V-243 - TEMP.
250
200
150
100
50
0
8 PM
10 PM
12 MN
2 AM

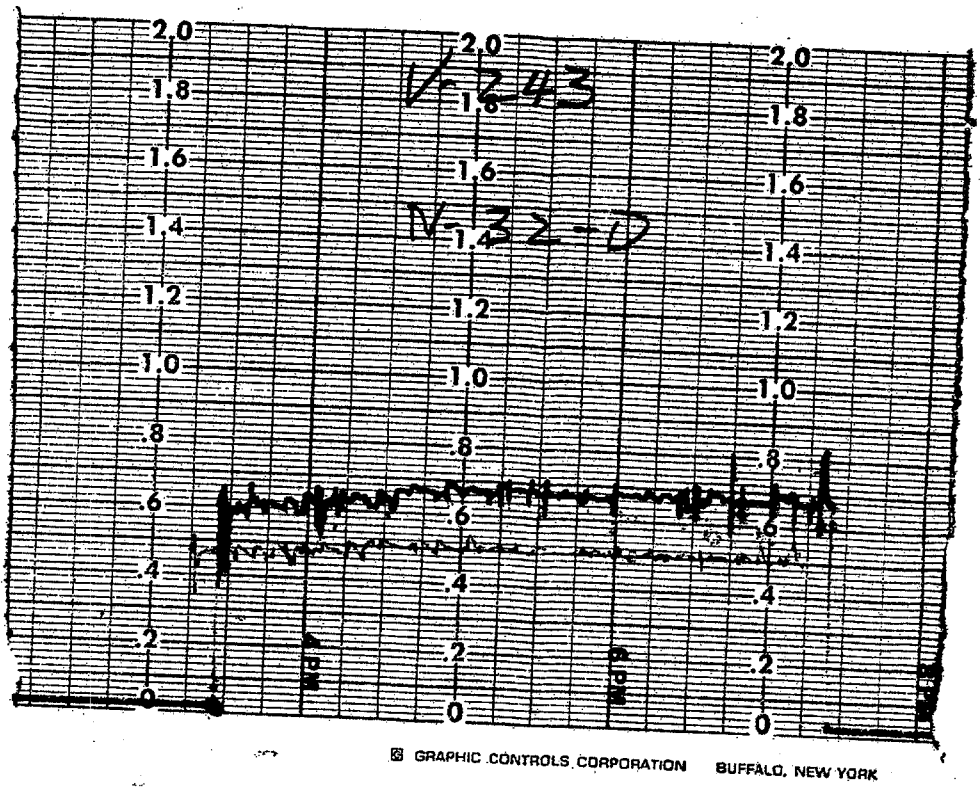
V-243
V-132-D
2.0
1.8
1.6
1.4
1.2
1.0
.8
.6
.4
.2
0
GRAPHIC CONTROLS CORPORATION BUFFALO, NEW YORK

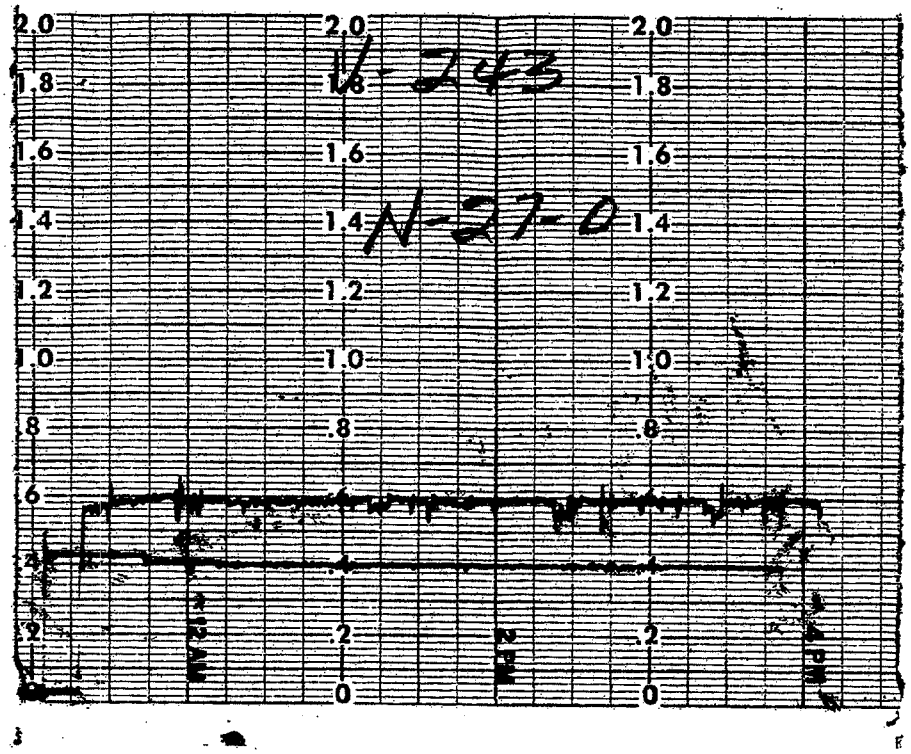
2.0
1.8
1.6
1.4
1.2
1.0
.8
.6
.4
.2
0
N-243
N-270
