TRACOMPANY CORRESPONDENCE
R-98 (Rev. 1-68)

PLAINTIFF'S EXHIBIT
RMC-458

FROM: J. F. Farrell - Baton Rouge

TO: Mr. P. L. Patty - Baton Rouge

COPY: Messrs: T. M. McCracken, J. A. Williams, F. C. Priest

DATE & SUBJECT: Progress Report - Job 7727 - W/E 11-30-74 December 2, 1974

Barnard & Burk personnel on site - 31
Betz personnel on site - 7
Leavesley-McCollum personnel on site - 18

No time lost due to labor or weather problems
One day lost because of Thanksgiving Holiday

Facility 24

Continue installation of walkway and miscellaneous steel, painting, piping and electrical work. Installing final steel and siding between combustion chamber and stack. New 3200# counterweight installed for combustion chamber damper door.

Leavesley completed kiln refractory and two of three kiln castable pours. Also completed castable raming in firing hood. Continuing installation of refractory in bottom section of stack.

Best Engineering 90% complete on remaining two stack sections.

Facility 24-A

Siding installation completed

Facility 35

Continue cooler drive installation. Pinion set and grouted. Cooler discharge equipment installation completed. Thirty inch transite vent dust installation completed.

Facility 40 - Complete

Facility 65 - Complete

Facility 66 - Completing punch list items. Turnover is still being held up by outstanding items on fire pump.

J. F. Farrell

JFF/gw

Attachment

INTRACOMPANY CORRESPONDENCE

R 98 (R... '/2)

FROM	J. F. Farrell - Baton Rouge
→ TO	Mr. P. L. Patty - Baton Rouge
COPY	Messrs: T. M. McCracken, J. A. Williams, F. C. Priest
DATE & SUBJECT	Progress Report - Job 7727 - W/E 1-4-75 January 6, 1975

Betz Electric personnel on site -2
Leavesley McCollum personnel on site - 7

Nichols Construction completed stack erection on 12-31-74 except for a few punch list items to be completed by Best Manufacturing Company.

Leavesley completed rigging of refractory platform in stack and began refractory installation on 1-2-75. Leavesley is having problems with brick hoist which is slowing progress. Refractory completion date is now scheduled for 1-17-75.

Instrumentation check out continuing.

J Farrell
J. F. Farrell

JFF/gw

RMC3300020000006

BARNARD & BURK, INC.

CONSTRUCTION DIVISION

P. O. BOX 18829 • BATON ROUGE, LOUISIANA

DATE 11-15-74

JOB NO. 7404

DAILY CONSTRUCTION REPORT

JOB NAME Reynolds Metals Co. LOCATION Baker, Louisiana

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND TIMEKEEPER. AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED Lee Nordan TIMEKEEPER

SIGNED K. A. Ford SUPERINTENDENT

WORKMEN	FOREMEN	MEN	TOTAL
PIPEFITTERS	1	5	6
IRON WORKERS	2	4	6
BOILER MAKERS	1	3	4
MILLWRIGHTS	1	3	4
CARPENTERS	1	2	3
OPERATORS	1	1	2
LABORERS	1	1	2
CEMENT FINISHERS		1	1
TRUCK DRIVERS		1	1
WAREHOUSE	1	1	2
OTHER: Painter	1	1	2
OFFICE STAFF	1	2	3
FIELD STAFF	1	1	2
CONSTRUCTION DIV. TOTAL	12	26	38
SUB-CONTRACTORS			
Betz Electric	1	7	8
GRAND TOTAL	13	33	46

EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
CRANES			
CHERRY PICKERS	1 1		12-15-74 12-31-74
PICK-UP TRUCKS	2		12-31-74
OTHER TRUCKS	1		12-15-74
WELDING MACHINES GAS & ELECT.	2 3		12-15-74 12-31-74
PIPE THREADING MACHINES			
AIR COMPRESSOR			
TEST PUMP			
BACKHOE			
JACKHAMMERS & TAMPERS			
SMALL TOOLS I.E. IMPACTS, DRILLS SKIL-SAWS	1		12-15-74
OFFICE TRAILER	1		12-31-74
CHANGE SHACKS	4 6		12-15-74 12-31-74
CUTTING RIGS			
OTHER:			
Sanitary Units		2 2	12-15-74 12-31-74
Tool boxes	2		12-15-74

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair:

Welding Wearing Strips on Cooler. Working on 30" Transite Duct. Erecting platforms on Combustion Chamber. Grouting Stack. Electricians pulling wire. Fabricating and erecting pipe. Painting structural steel. General clean-up. Recieving materials.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS)

Complete 30" Transite Duct. Will continue setting Penion Gear & Drive for Cooler. Finnish welding Wearing Strips on Cooler. Erect platform, handrails, and grating, north and west side of Combustion Chamber. Grouting Stack Foundation. Trimming and flashing Comtrol House. Install seals on Cooler. Continue painting structural steel. Fabricate and erect pipe. Electricians pulling wire, setting motors, running conduit. General clean-up. Recieving materials.

CHANGE ORDER ALERT (DESCRIBE BRIEFLY)

DISTRIBUTION:

MGR. OF CONST. _____ PLANT SCHED. _____

ENGINEERING _____ COST CONTROL _____

PURCHASING _____ EQUIP. MGR. _____

SIGNED _____ OWNER (WHEN APPLICABLE)

RMC3300020000007

BARNARD & BURK, INC.
CONSTRUCTION DIVISION
P. O. BOX 15629 • BATON ROUGE, LOUISIANA

DATE 11-22-74

JOB NO 7404

DAILY CONSTRUCTION REPORT

JOB NAME Reynolds Metals Co. LOCATION Baker, Louisiana

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND TIMEKEEPER, AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED [illegible] TIMEKEEPER SIGNED [illegible] SUPERINTENDENT

WORKMEN	FOREMEN	MEN	TOTAL
PIPEFITTERS	1	5	6
IRON WORKERS	1	6	7
BOILER MAKERS	1	3	4
MILLWRIGHTS	1	3	4
CARPENTERS	1	1	2
OPERATORS	1	1	2
LABORERS	1	1	2
CEMENT FINISHERS		1	1
~~TRUCK DRIVERS~~ S.M.		1	1
WAREHOUSE	1	1	2
OTHER: Painter		1	1
OFFICE STAFF	1	1	2
FIELD STAFF	1	1	2
CONSTRUCTION DIV. TOTAL	10	26	36
SUB-CONTRACTORS			
Betz Electric	1	7	8
GRAND TOTAL	11	33	44

EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
CRANES			
CHERRY PICKERS	1 1		12-15-74 12-31-74
PICK-UP TRUCKS	2		12-31-74
OTHER TRUCKS	1		12-15-74
WELDING MACHINES GAS & ELECT.	2 3		12-15-74 12-31-74
PIPE THREADING MACHINES			
AIR COMPRESSOR			
TEST PUMP			
BACKHOE			
JACKHAMMERS & TAMPERS			
SMALL TOOLS I.E. IMPACTS DRILLS, SKIL-SAWS	1		12-15-74
OFFICE TRAILER	1		12-31-74
CHANGE SHACKS	4 6		12-15-74 12-31-74
CUTTING RIGS			
OTHER:			
Sanitary Units		2 2	12-15-74 12-31-74
Tool boxes	2		12-15-74

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair:

Fabricated steel beam and poured counterwieghts. Erectin 30" Transite duct. Erecting steel platforms & handrails. Triming out Control bldg. roof, siding. Triming out Combustion Chamber siding. Fabricating and erecting pipe. Pulling wire. running conduit. Painting structural steel. aligning Bull Gear to Cooler.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS)

Starting Kiln motor and Drive. Installing guards & Seals on Kiln. Erect handrails & stair treads. General clean-up. Recieving materials.

RMC3300020000008

BARNARD & BURK, INC.
CONSTRUCTION DIVISION
P. O. BOX 18629 • BATON ROUGE, LOUISIANA

DATE 9-20-74 Fri

DAILY CONSTRUCTION REPORT

JOB NO. 7404

JOB NAME Reynolds Metals Co LOCATION Baker, Louisiana

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND TIMEKEEPER, AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED Lee Hawkins TIMEKEEPER SIGNED R. A. Font SUPERINTENDENT

WORKMEN	FOREMEN	MEN	TOTAL
PIPEFITTERS	1	3	4
IRON WORKERS	3	14	17
BOILER MAKERS	1		1
MILLWRIGHTS	1	9	10
CARPENTERS	1	5	6
OPERATORS	1	3	4
LABORERS	1	5	6
CEMENT FINISHERS		1	1
~~TRUCK DRIVERS~~ PT	1		1
WAREHOUSE	1	2	3
OTHER: Rodman		1	1
OFFICE STAFF	1	3	4
FIELD STAFF	1	1	2
CONSTRUCTION DIV. TOTAL	13	47	60
SUB-CONTRACTORS			
Betz Elect	1	5	6
GRAND TOTAL	14	52	66

EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
CRANES			
CHERRY PICKERS	2		
PICK-UP TRUCKS	2		
OTHER TRUCKS	1		
WELDING MACHINES GAS & ELECT.	6		
PIPE THREADING MACHINES			
AIR COMPRESSOR	1		
TEST PUMP			
BACKHOE	1		
JACKHAMMERS & TAMPERS	2		
SMALL TOOLS I.E. IMPACTS, DRILLS, SKIL-SAWS	5	x	
OFFICE TRAILER	1		
CHANGE SHACKS	9		
CUTTING RIGS	4		
OTHER:			
Sanitary Units		4	
Tool Boxes	2		

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair: Excavating and forming transite duct piers, catwalk piers and furnace piers. Building forms and pouring concrete for furnace piers. Also pouring concrete for drain trench. Welding kiln thrust tire rings. Installing and aligning gear flange on kiln. Aligning thrust tire. Aligning the lower kiln tire. Continue installing sheeting on combustion chamber. Installing catwalk steel. Electrical contractor running conduit for kiln control house. Unloading materials and machinery.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS)

Continue excavating and forming transite duct piers, catwalk piers and furnace piers. Building forms and pouring concrete for furnace piers. Continue pouring concrete for drain trench. Continue welding kiln thrust tire rings. Continue installing and aligning gear flange on kiln. Continue aligning thrust tire. Continue aligning the lower kiln tire. Continue installing sheeting on combustion chamber. Continue installing catwalk steel. Electrical contractor still running conduit for kiln control house. Continue unloading materials and machinery.

CHANGE ORDER ALERT (DESCRIBE BRIEFLY)

DISTRIBUTION:
MGR. OF CONST. _____ PLAN & SCHED. _____
ENGINEERING _____ COST CONTROL _____
PURCHASING _____ EQUIP. MGR. _____

SIGNED _____ OWNER (WHEN APPLICABLE)

RMC3300020000009

CONSTRUCTION DIVISION

P. O. BOX 15629 • BATON ROUGE, LOUISIANA

DAILY CONSTRUCTION REPORT

DATE 8-30-74 Fri

JOB NO. 7404

JOB NAME Reynolds Metals Co. LOCATION Baker, La.

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND TIMEKEEPER, AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED Paul Glansonne TIMEKEEPER

SIGNED K. A. Font SUPERINTENDENT

WORKMEN	FOREMEN	MEN	TOTAL
PIPEFITTERS	1		1
IRON WORKERS	3	14	17
BOILER MAKERS			
MILLWRIGHTS	1	3	4
CARPENTERS	1	10	11
OPERATORS	1	6	7
LABORERS	1	11	12
CEMENT FINISHERS		1	1
TRUCK DRIVERS			
WAREHOUSE	1	2	3
OTHER: Rodman		1	1
OFFICE STAFF	1	3	4
FIELD STAFF	2	1	3
CONSTRUCTION DIV. TOTAL	12	52	64
SUB-CONTRACTORS			
Betz Elect	1	5	6
GRAND TOTAL	13	57	70

EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
CRANES			
CHERRY PICKERS	2		
PICK-UP TRUCKS	3		
OTHER TRUCKS	1		
WELDING MACHINES GAS & ELECT.	5		
PIPE THREADING MACHINES			
AIR COMPRESSOR	1		
TEST PUMP			
BACKHOE	1		
JACKHAMMERS & TAMPERS	2		
SMALL TOOLS I.E. IMPACTS, DRILLS, SKIL-SAWS	5		
OFFICE TRAILER	1		
CHANGE SHACKS	9		
CUTTING RIGS	4		
OTHER:			
Sanitary Units		4	
Tool Boxes	2		

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair A.M.--Welding out kiln. Kiln aligned. Forming drain trench and footings for transite duct and catwalk piers. Excavating for furnace piers. Unloading materials and machinery. Electricians on job site. Alining and welding tires on cooler.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS)

Continue installing and welding kiln sections. Continue aligning kiln and cooler tires. Start installing ring gear on kiln and cooler. Continue forming and pouring forms for footings and kiln control house. Continue unloading and checking materials. Continue unloading machinery. Electrical contractor to continue conduit runs.

CHANGE ORDER ALERT (DESCRIBE BRIEFLY)

DISTRIBUTION:

MGR. OF CONST. _____ PLAN & SCHED. _____

ENGINEERING _____ COST CONTROL _____

PURCHASING _____ EQUIP. MGR. _____

SIGNED _____ OWNER (WHEN APPLICABLE)

RMC3300020000010

INTRACOMPANY CORRESPONDENCE

R-98 (Rev. 1-68)

FROM:	J. F. Farrell - Baton Rouge
→ TO:	Mr. P. L. Patty - Baton Rouge
COPY:	Messrs: T. M. McCracken, J. A. Williams, F. C. Priest
DATE & SUBJECT:	Progress Report - Job 7727 - W/E 6-29-74 — June 29, 1974

No time lost due to weather or labor problems.

Facility Y.0 - no progress

Facility 24.0

Continue forming pier "A" walls and erection of combustion chamber. Poured 30" transite duct footing at pier "B".

Facility 35.0

Setting of cooler trunions and installing riding rings on cooler. Continue excavation for conveyor trench extension.

Facility 31.0 - Hold

Facility 40.0 - Complete

Facility 65.0 - Complete

Facility 66.0

Poured fire pump and fire pumphouse foundation.

J. F. Farrell

JFF/gw

BARNARD & BURK, INC.

CONSTRUCTION DIVISION

P. O. BOX 15629 • BATON ROUGE, LOUISIANA

DATE 7-3-74 WED

DAILY CONSTRUCTION REPORT

JOB NO. 7404

JOB NAME Reynolds Metals LOCATION Baker, La.

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND FINANCIER, AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED [signature] TIMEKEEPER SIGNED K. A. Fontaine SUPERINTENDENT

WORKMEN	FOREMEN	OTHER	TOTAL	EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
PIPEFITTERS	1		1	CRANES			
IRON WORKERS	2	11	13	CHERRY PICKERS	2		
BOILER MAKERS BL	1		1	PICK-UP TRUCKS	2		
MILLWRIGHTS	1	1	2	OTHER TRUCKS	1		
CARPENTERS	1	11	12	WELDING MACHINES GAS & ELECT.	1		
OPERATORS	1	3	4	PIPE THREADING MACHINES			
LABORERS	1	11	12	AIR COMPRESSOR	1		
CEMENT FINISHERS		1	1	TEST PUMP			
TRUCK DRIVERS		1	1	BACKHOE	1		
WAREHOUSE	1	2	3	JACKHAMMERS & TAMPERS	2		
OTHER: Rodman		1	1	SMALL TOOLS I.E. IMPACTS, DRILLS, SKIL-SAWS	5		
OFFICE STAFF	1	3	4	OFFICE TRAILER	1		
FIELD STAFF	2	1	3	CHANGE SHACKS	8		
CONSTRUCTION DIV. TOTAL	12	46	58	CUTTING RIGS	2		
SUB-CONTRACTORS				OTHER:			
Retz Electric	1	1	2	Sanitary Unit		4	
				Tool Boxes	2		
GRAND TOTAL	13	47	60				

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair

Erecting structural steel for combustion chambers. Pouring kiln pier A walls and kiln drive pier wall. Pouring slab for conveyor trench. Excavating kiln control house footings. Setting sub-sole plates for cooler trunions. Cleaning cooler pads for siding rings. Unloading materials. Electrical Contractor doing temporary electrical work.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS) Continue forming and pouring concrete for kiln pier A and kiln drive pier. Form conveyor trench walls. Continue excavating and pouring footings for transite duct and kiln control house and cooler building footings. Continue setting blocks for pump house. Continue setting siding rings and carriage rolls for cooler. Continue unloading materials and machinery. Electrical Contractor to make conduit runs from pier A to pier B, etc.

CHANGE ORDER ALERT (DESCRIBE BRIEFLY)

DISTRIBUTION:

MGR. OF CONST. _____ PLAN & SCHED. _____

ENGINEERING _____ COST CONTROL _____

PURCHASING _____ EQUIP. MGR. _____

SIGNED _____ OWNER (WHEN APPLICABLE)

RMC3300020000012

BARNARD & BURK, INC.
CONSTRUCTION DIVISION
P. O. BOX 15629 • BATON ROUGE, LOUISIANA

DATE 6-21-74 FRI

DAILY CONSTRUCTION REPORT

JOB NO. 7404

JOB NAME Reynolds Metals LOCATION Baker, La.

DAILY LETTER SHALL BE WRITTEN BY THE TIMEKEEPER AND SIGNED BY BOTH THE SUPERINTENDENT AND TIMEKEEPER, AND EACH WILL BE HELD RESPONSIBLE FOR ACCURACY OF THIS LETTER AND FOR OMISSION OF ANY FACTS WHICH THE MAIN OFFICE SHOULD KNOW. WE SOLICIT SUGGESTIONS FOR INCREASING EFFICIENCY AND SPEED.

SIGNED Paul Giansonne TIMEKEEPER

SIGNED K A Font SUPERINTENDENT

WORKMEN	FOREMEN	MEN	TOTAL
PIPEFITTERS	1		1
IRON WORKERS	2	8	10
BOILER-MAKERS- PTR	1	1	2
MILLWRIGHTS			
CARPENTERS	1	12	13
OPERATORS	1	3	4
LABORERS	1	10	11
CEMENT FINISHERS		1	1
TRUCK DRIVERS		3	3
WAREHOUSE	1	1	2
OTHER: Rodman		1	1
OFFICE STAFF	1	3	4
FIELD STAFF	2	1	3
CONSTRUCTION DIV. TOTAL	11	44	55
SUB-CONTRACTORS			
Betz Electric	1		1
GRAND TOTAL	12	44	56

EQUIPMENT	CO. OWNED	OUTSIDE RENTAL	PROJECTED END DATE
CRANES			
CHERRY PICKERS	2		
PICK-UP TRUCKS	2		
OTHER TRUCKS	1		
WELDING MACHINES GAS & ELECT.	1		
PIPE THREADING MACHINES			
AIR COMPRESSOR	1		
TEST PUMP			
BACKHOE	1		
JACKHAMMERS & TAMPERS	2		
SMALL TOOLS I.E. IMPACTS, DRILLS, SKIL-SAWS	5		
OFFICE TRAILER	1		
CHANGE SHACKS	7		
CUTTING RIGS	2		
OTHER:			
Sanitary Units		4	
Fork Lift		2	

MATERIAL NEEDED

DRAWINGS OR INFORMATION NEEDED

WORK ITEMS ACCOMPLISHED THIS DAY

WEATHER: Fair

Excavating for footing foundations at control building and piers B. Forming walls for kiln pits A. Excavating for conveyor trench. Breaking out existing concrete at conveyor trench. Erecting structural steel for combustion chamber building. Backfilling 8" fire water line at pump house.

ACTIVITY DURING NEXT 7 DAYS: (INCLUDING SUB-CONTRACTORS) Continue forming and pour concrete for kiln pier A walls. Form and pour footings for 36" trapsite line and control building. Continue erecting structural steel for combustion chamber building and start bolting up the building. Continue unloading materials and machinery. Electrical Contractor to start conduit runs from pier A to pier B.

CHANGE ORDER ALERT (DESCRIBE BRIEFLY)

DISTRIBUTION:
MGR. OF CONST. _____ PLAN & SCHED. _____
ENGINEERING _____ COST CONTROL _____
PURCHASING _____ EQUIP. MGR. _____

SIGNED _____
OWNER (WHEN APPLICABLE)

RMC3300020000013

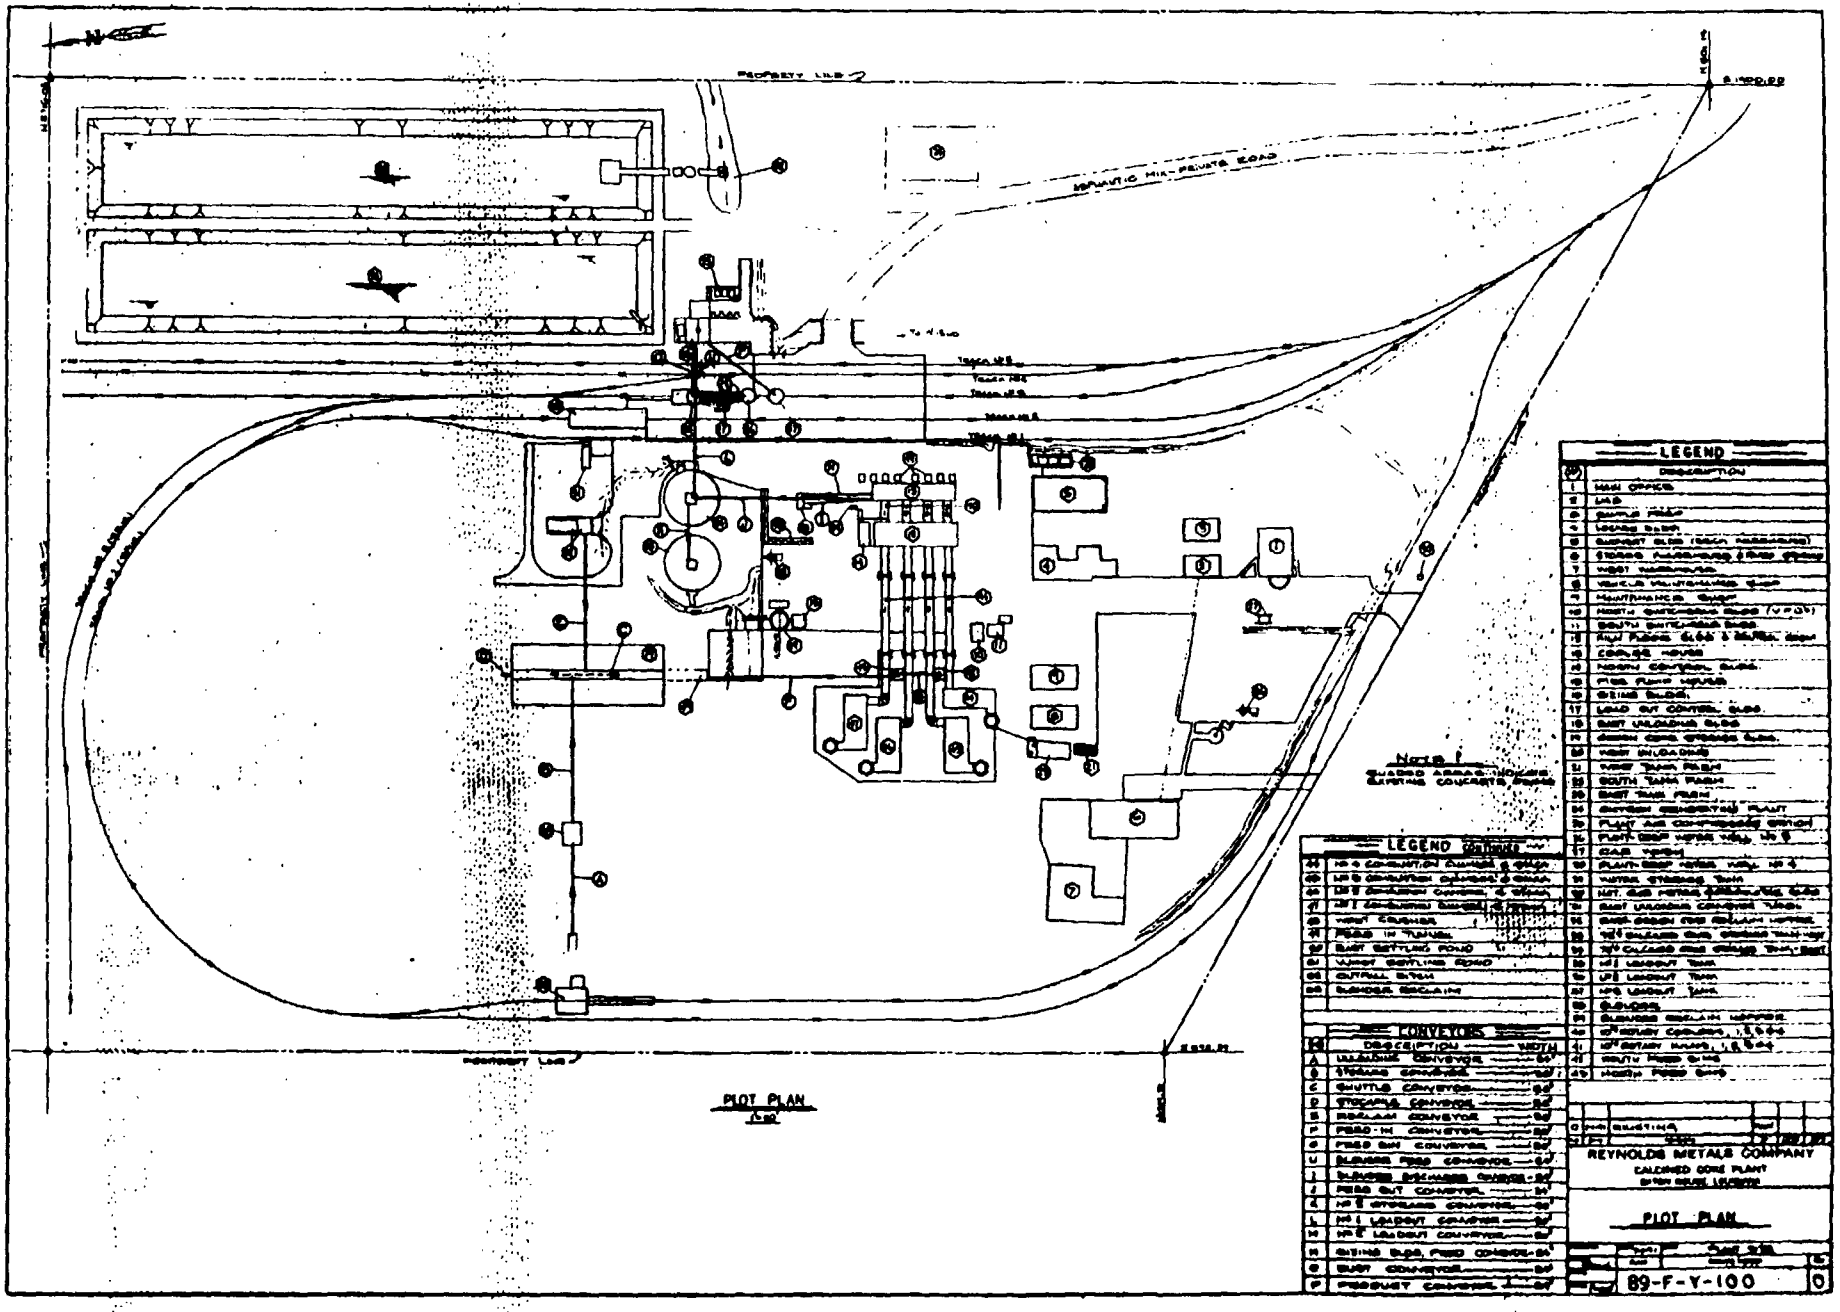

RMC330002000001

CONTRACT CHANGE REQUEST

BARNARD & BURK, INC.
CONSTRUCTION DIVISION
P. O. BOX 15828
BATON ROUGE, LOUISIANA 70815

Contract No.	Contractor's Job No.	Change Request No.
58386-M	7404	16

JOB TITLE: Coke Plant Expansion

CUSTOMER'S NAME: Reynolds Metals Co.

EXTRA WORK
THE FOLLOWING CONTRACT CHANGE REQUEST IS SUBMITTED FOR YOUR APPROVAL:

1. DESCRIPTION OF WORK:

Refabricate steel span for transite pipe at south side of control building span interferred with biulding girts and siding. Moved north span member appros. 4" south and shortened lateral braces and struts.

4 I.W.	4 days	=	128 M.H.
1 Op.	2 days	=	16 M.H.
Estimated Total			144 M.H. @ $11 = $1584

Drawing Error

2. LUMP SUMP PRICE:

$1584.00

3. CONTRACT EXTENSION REQUESTED FOR ABOVE WORK:

Customer's Representative	Date	Contractor's Representative	Date
J Harrell	11-22-74	K. A. Font	11-22-74

RMC3300020000002

CONTRACT CHANGE REQUEST

BARNARD & BURK, INC.
CONSTRUCTION DIVISION
P. O. BOX 18628
BATON ROUGE, LOUISIANA 70815

Contract No.	Contractor's Job No.	Change Request No.
58386-M	7404	22

JOB TITLE: Coke Plant Expansion

CUSTOMER'S NAME: Reynolds Metals Co.

THE FOLLOWING CONTRACT CHANGE REQUEST IS SUBMITTED FOR YOUR APPROVAL:

1. DESCRIPTION OF WORK:

Change 30" transite duct bridge footing at S.E. corner of control bldg.

5 lab.	1 day	=	40 M.H.
4 Carp.	1 day	=	32 M.H.
2 I.W.	½ day	=	8 M.H.
5 Lab.	¼ day	=	10 M.H.
1 Cem. M.	¼ day	=	2 M.H.
1 I.W.	¼ day	=	2 M.H.
1 Carp.	¼ day	=	2 M.H.
Estimate Total			96 M.H. @ $11 = $1056

Eng. Error concrete to steel drawing discrepancy

2. LUMP SUMP PRICE:
$1056.00

3. CONTRACT EXTENSION REQUESTED FOR ABOVE WORK:

Customer's Representative	Date	Contractor's Representative	Date
J Harrell	11-22-74	K. A. Hunt	11-22-74

RMC3300020000003

INTRACOMPANY CORRESPONDENCE

R-98 (Rev. 1-45)

FROM:	J. F. Farrell - Baton Rouge
→ TO:	Mr. P. L. Patty - Baton Rouge
COPY:	Messrs: T. M. McCracken, J. A. Williams, F. C. Priest
DATE & SUBJECT:	Progress Report - Job 7727 - W/E 12-28-74 — December 31, 1974

Barnard & Burk personnel on site as of 12-24-74 - 11
Betz personnel on site as of 12-24-74 - 2
Leavesley McCollum personnel on site as of 12-24-74 - 2

Barnard & Burk move-out completed on Christmas eve, 12-24-74, with the exception of the office trailer and one cherry picker. All facilities completed and turned over to the Plant as of 12-24-74.

Nichols is continuing to erect the stack and should be complete by 12-31-74.

Leavesley-McCollum brought two men on site to build a platform for installing stack refractory. Refractory installation should begin on 1-2-75 and should be completed for startup on 1-15-75.

Instrumentation and electrical check-out is being done with two electricians from Betz Electric under the Plant maintenance agreement.

J. F. Farrell

JFF/gw

RMC3300020000004
