
FILE NAME: Hopeman Brothers (HB)

DATE: 1945 Apr 12

DOC#: HB025

DOCUMENT DESCRIPTION: Material Requisition Order Forms

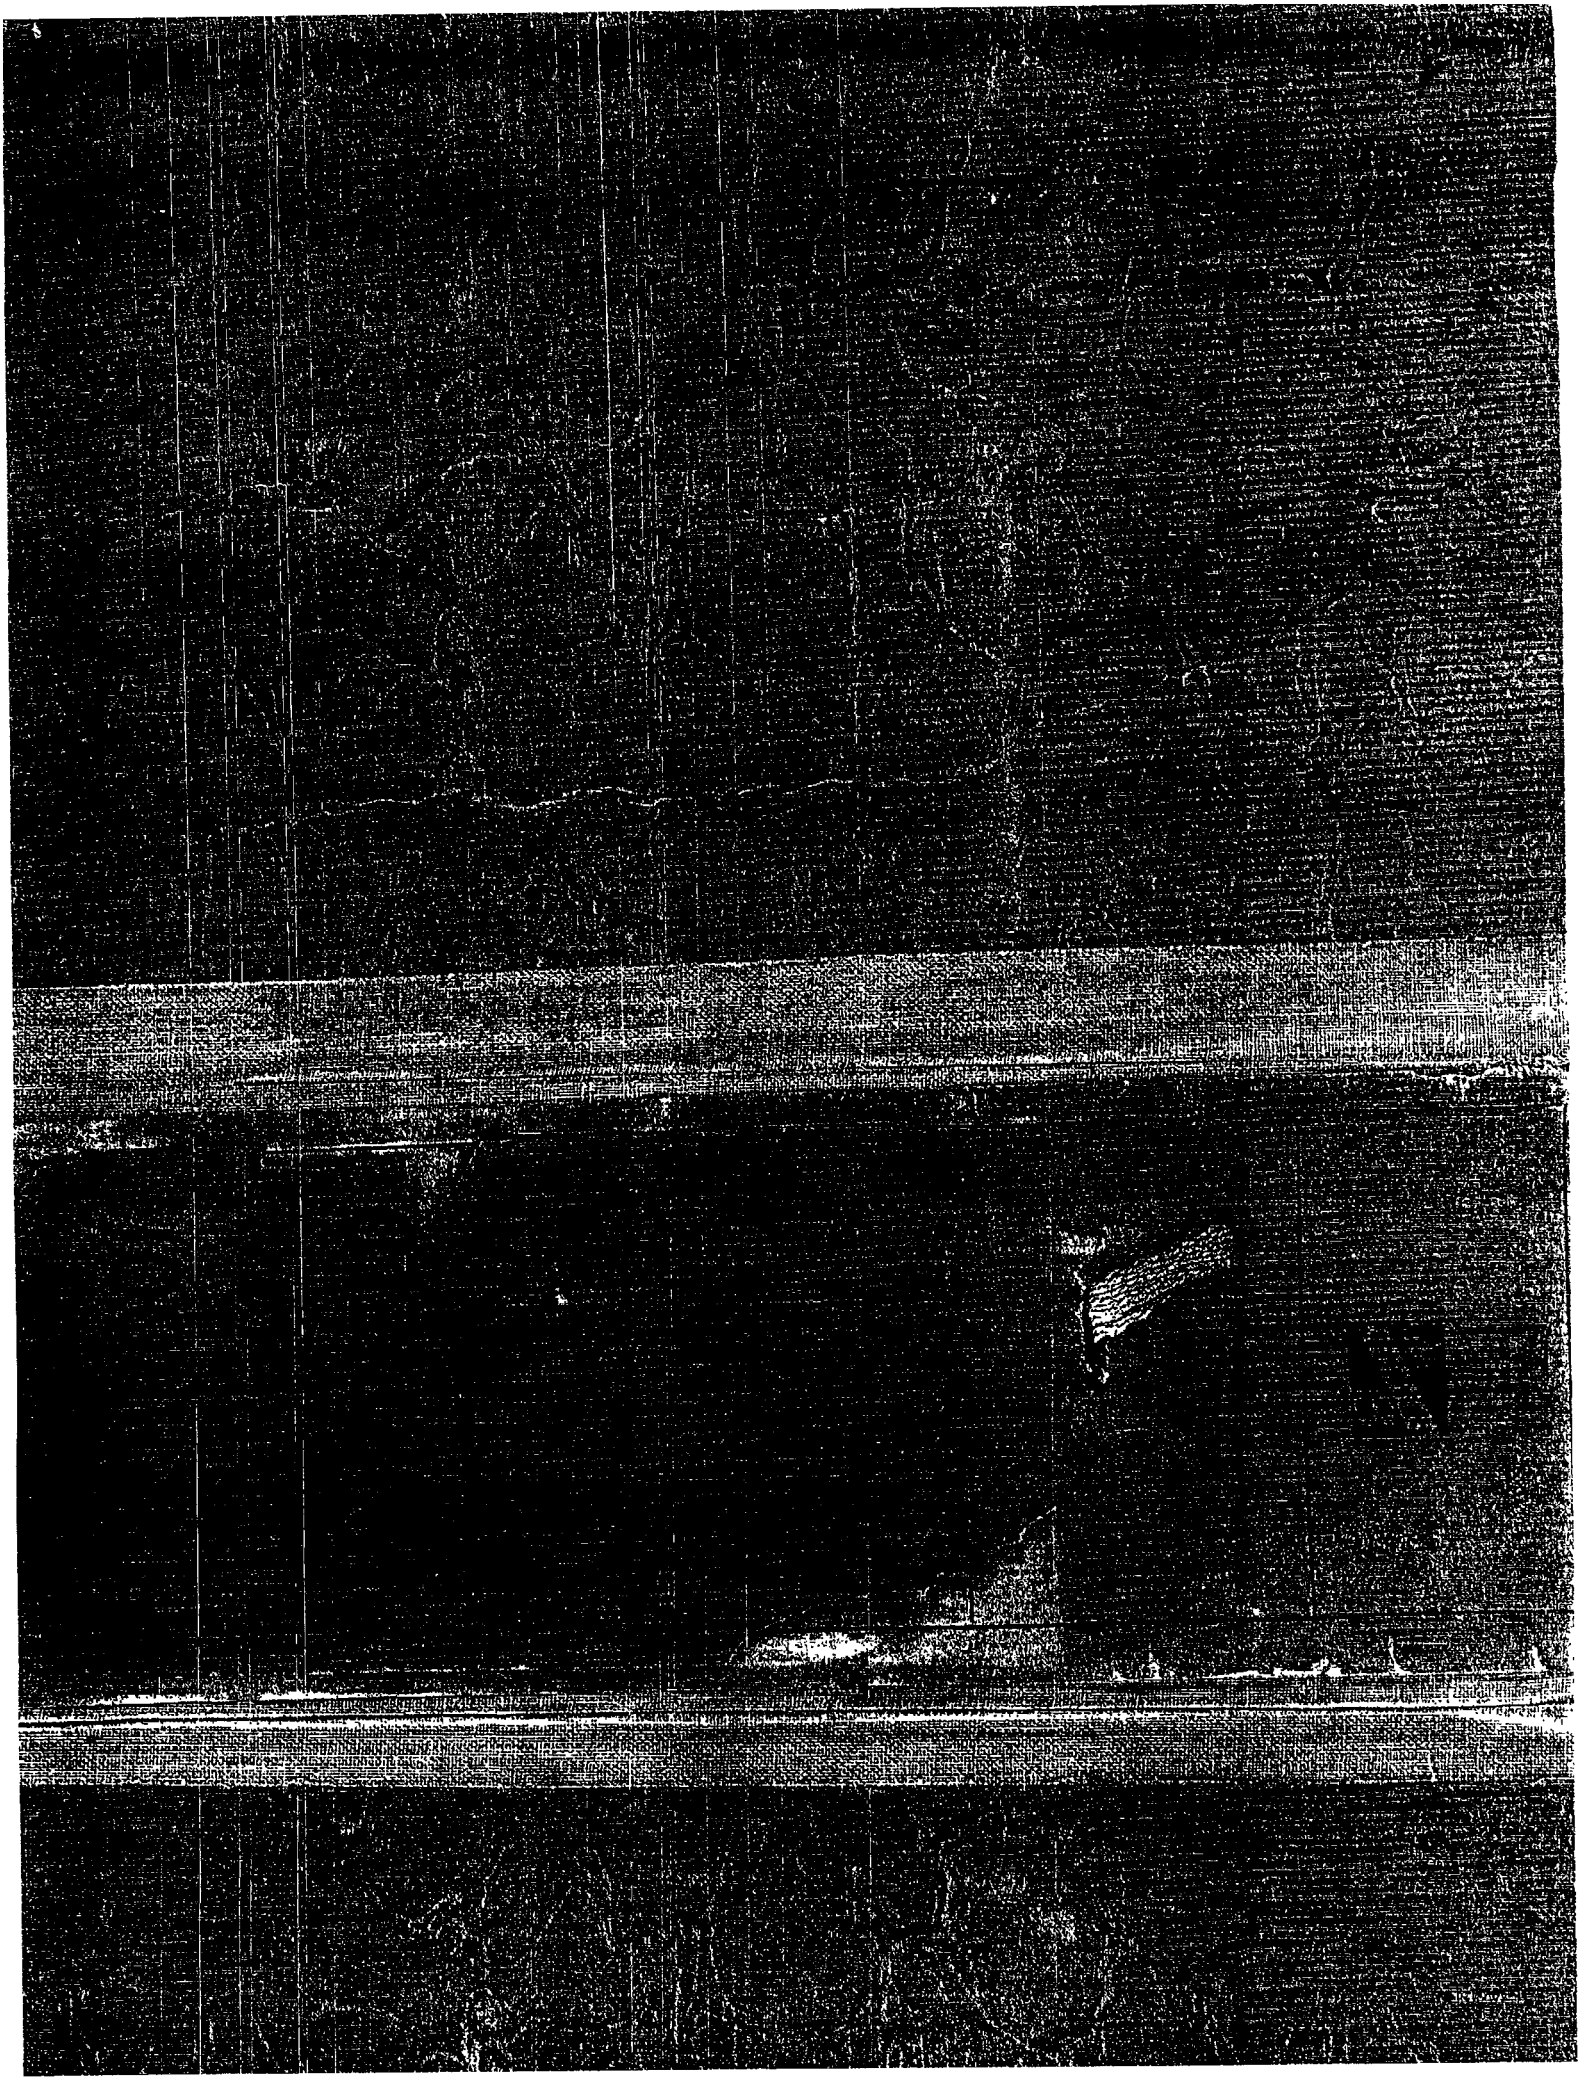

MATERIAL REQUISITION

A

DATE REQUIRED

TOTAL REQ.	QUAN. PER SHIP	DESCRIPTION	DATE ORDERED	VENDOR	P. O NUMBE
		Insulation in way of W. Tanks			
		as per Sk # 206			

PROVED

PROVED

CONTRACT VICTORY FIREPROOF CARGO

DELIVER TO FAIRFIELD 20 ADDITIONAL

DATE ISSUED 4-12-45

REVISION 1

2

3

MATERIAL REQUISITION

A

DATE REQUIRED

TOTAL REQ.	QUAN. PER SHIP	DESCRIPTION	DATE ORDERED	VENDOR	P. O. NUMBE
		Ceiling Insulation			
		as per Sk # 205			

PROVED

PROVED

CONTRACT VICTORY FIREPROOF CARGO

DELIVER TO FAIRFIELD 20 ADDITIONAL

DATE ISSUED 4-12-45

REVISION 1

2

3

MATERIAL REQUISITION

A

DATE REQUIRED

TOTAL REQ.	QUAN. PER SHIP	DESCRIPTION	DATE ORDERED	VENDOR	P. O. NUMBE
		Wardrobe Rods & Flanges			
		as per Sk # 163			

PROVED

PROVED


CONTRACT VICTORY FIREPROOF CARGO

DELIVER TO FAIRFIELD 20 ADDITIONAL

DATE ISSUED 4-12-45

REVISION 1

2

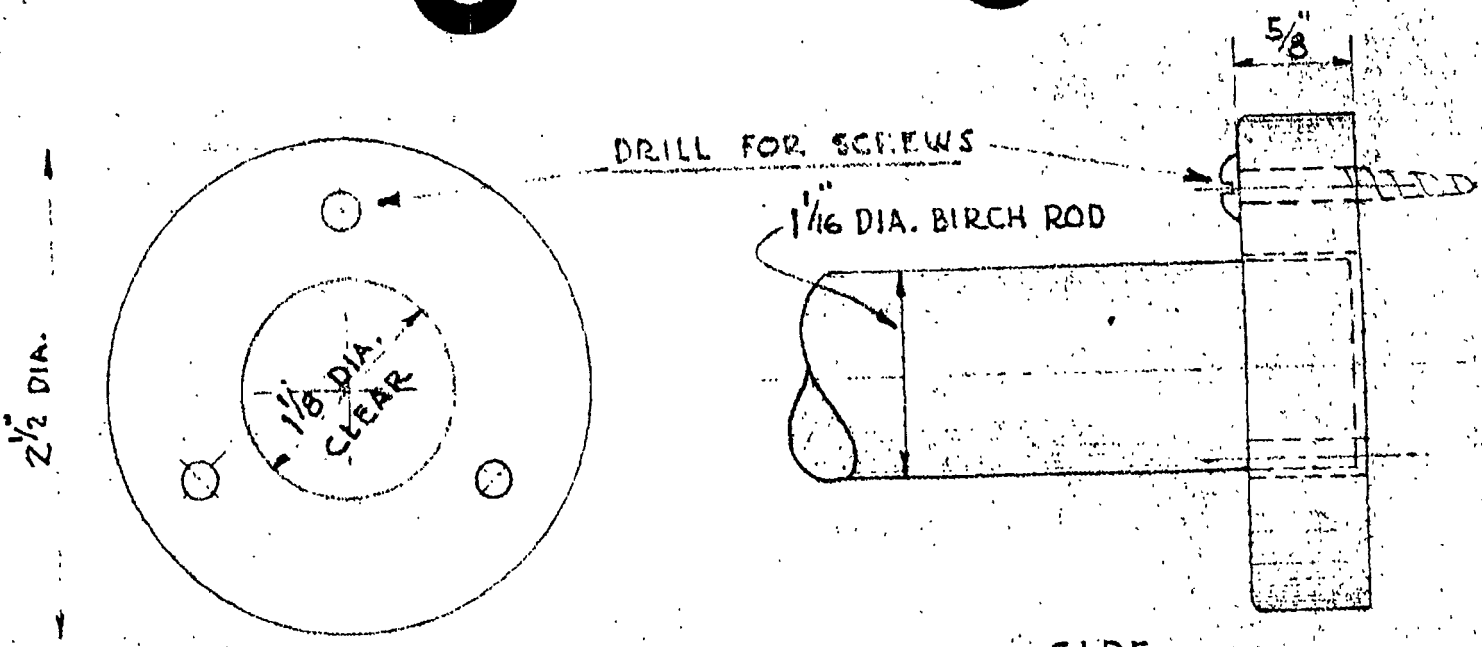


MAKE (50) FLANGES AS SHOWN

MAKE	(1)	ROD	4' - 10"	LONG	FOR	WARDROBE #	210
"	1	"	3' - 1"	"	"	"	211
"	1	"	4' - 10"	"	"	"	212
"	1	"	3' - 6"	"	"	"	213
"	1	"	4' - 1"	"	"	"	214
"	1	"	3' - 4"	"	"	"	215
"	1	"	3' - 4"	"	"	"	216
"	1	"	4' - 10"	"	"	"	217-218
"	1	"	4' - 10"	"	"	"	219-220
"	1	"	3' - 2"	"	"	"	229
"	1	"	5' - 0"	"	"	"	230-231
"	1	"	3' - 4"	"	"	"	232
"	1	"	2' - 5"	"	"	"	233
"	1	"	2' - 5"	"	"	"	234
"	1	"	3' - 10"	"	"	"	235
"	1	"	3' - 1"	"	"	"	237
"	1	"	5' - 0"	"	"	"	238-239
"	1	"	3' - 5"	"	"	"	246
"	1	"	3' - 6"	"	"	"	247-248


MAKE 190 LIN. FEET OF ROD — TO BE CUT TO LENGTHS AS LISTED AT JOB

MATERIAL - ALL BIRCH

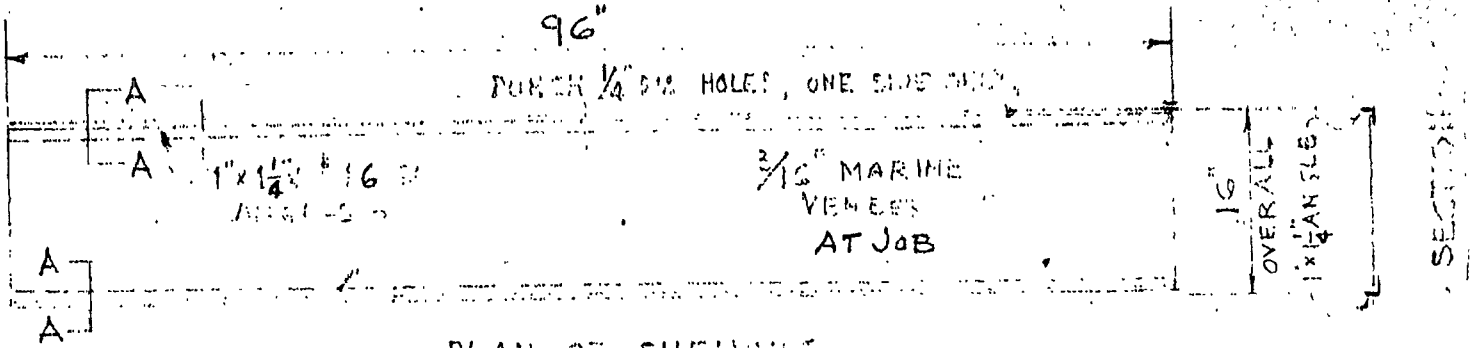

PLAN OF SHELVING

SCALE: 3/4" = 1'-0"

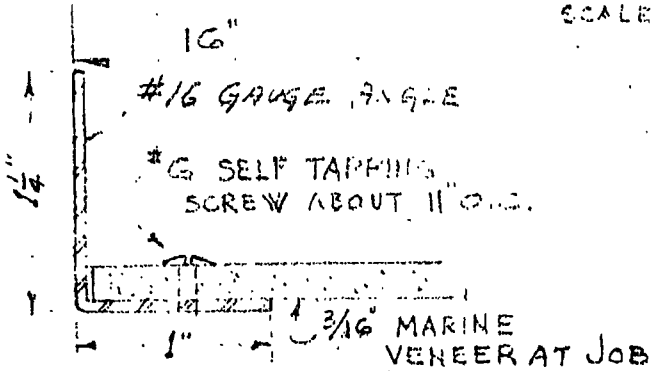

F.S. SECT. "A"-"A"


REQUIRED: 10-PCS. OF SHELVING 8'-0" LONG AS SHOWN.

MATERIAL: AS SHOWN.


FINISH: ANGLES ONLY TO BE PRIME COATED.

ALSO -

4-PCS. 9 1/2" WIDE x 84" LONG.

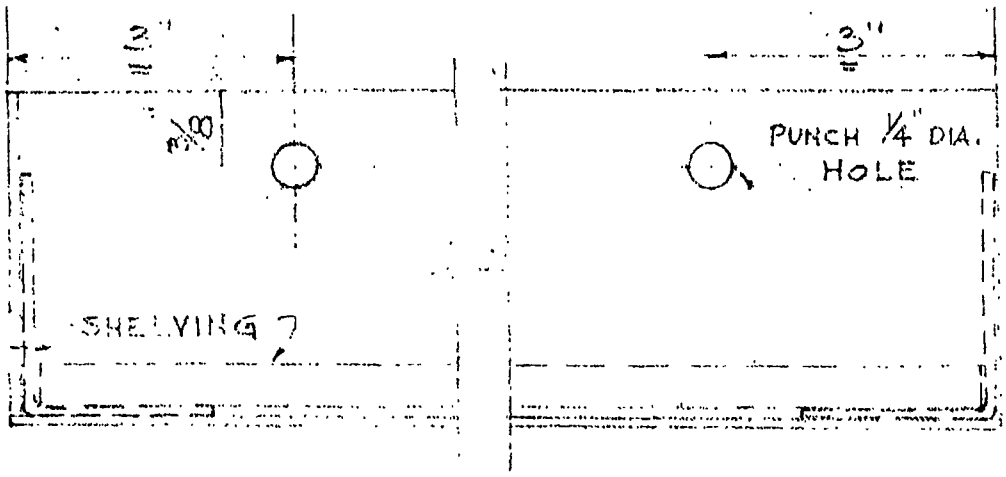

ELEVATION

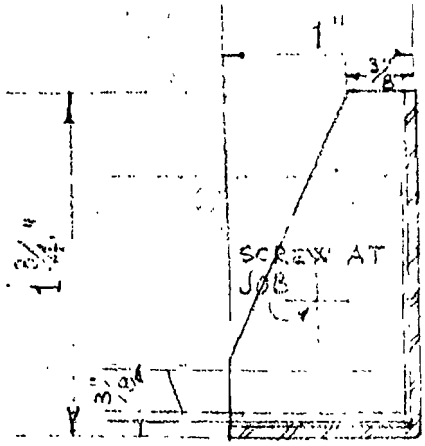

SECTION

16"

PROVIDE SLOTS FIT FOR SHELVING

SHELVING

MATERIAL: 1"x1 3/4" x 18 GA. ANGLES

FINISH: STANDARD PRIMER.

PLAN OF ANGLE FOR ENDS OF SHELVING

MAKE: 25 PRS. OF ANGLES FOR SHELVING AS SHOWN

FURNISH:

QUANTITY		WIDTH	LENGTH
11	PANELS	42" X	86½"
3	"	40" X	"
3	"	38" X	"
58	"	36" X	"
11	"	34" X	"
3	"	33" X	"
4	"	32" X	"
2	"	31" X	"
2	"	30½" X	"
2	"	30" X	"
2	"	28" X	"
2	"	27" X	"
3	"	26" X	"
2	"	25" X	"
4	"	22" X	"
7	"	21" X	"
2	"	20" X	"
1	"	19" X	"
3	"	18" X	"
4	"	16" X	"
1	"	15" X	"
2	"	14" X	"
2	"	13" X	"
5	"	12" X	"
1	"	10" X	"
1	"	9" X	"
4	"	6" X	"
1	"	2½" X	"
42	"	29½" X	43½"

ALL ½" THICK GYPSUM METAL ONE SIDE

QUANTITY GIVEN FOR ONE SIDE

FURNISH:

QUANTITY		WIDTH LENGTH
37	PANELS	42" X 86½"
4	"	40" X "
2	"	37½" X "
79	"	36" X "
3	"	35" X "
3	"	34" X "
6	"	32" X "
3	"	30" X "
1	"	29" X "
1	"	28" X "
1	"	27" X "
1	"	26" X "
1	"	25½" X "
7	"	24" X "
14	"	23" X "
9	"	22" X "
4	"	21" X "
5	"	20" X "
1	"	19" X "
2	"	18" X "
1	"	17" X "
2	"	15" X "
4	"	14" X "
2	"	13" X "
5	"	12" X "
2	"	11" X "
2	"	10" X "
5	"	9" X "
1	"	8" X "
2	"	7" X "
3	"	6" X "
2	"	4" X "

ALL ⅞" THICK GYPSUM METAL TWO SIDES
