CG-16 CODE RT-759-D PKG 59 PROCESSES APPROVED BY:
10/8/82 K2379 2555 LBS. ( ) RT-759-D (L) BBK 11/10/81
( DATE ) ( LOT ) ( EST WT ) COMTYP JOB NAME: 16RT759DML

STANDARD HRS. _____ TIME 7A M

LOT G102, 2600 #, 26 DRUMS

PREPARATION NOTES: _____

| EQUIPMENT | | NAME: MONASTRAL RED Y 1 PAGE | USE LBS | N-CODE | ACCT LBS |
|---|---|---|---|---|---|
| | | NOTE: (1) THIS FORMULA IS DESIGNED TO PROCESS +/- 2600# OF N-7529-A TO THE NEAREST FULL DRUM<br>(2) RECORD ACCOUNT POUNDS 2600<br>(3) CALCULATE EST WT. = ACCT LBS X 0.983 | | | |
| MISC 1 | 1 | OBTAIN FOR S4<br>LOT G/102 % 99.9 NET WT 2600 100% WT 2556 | 2600 | 7529-A | 2600 |
| 282 2 | 2 | INSTALL TEMP CHART IN V-282 & RUN IN 30" | | | |
| | 2 | (3000G) WATER | | | |
| | 3 | HEAT TO 140-150 DEG F IN 40-50 MIN & SHUT OFF STEAM | | | |
| | 4 | PUMP IN N-7529-A FROM S1 | | | |
| | 5 | FLOOD TO 86" (8505G) & STOP AGITATOR<br>START 4:45 PM FIN 8:30 PM OPERATOR LH | | | |

OCT 13 1982

10/12/82

DUP050103514

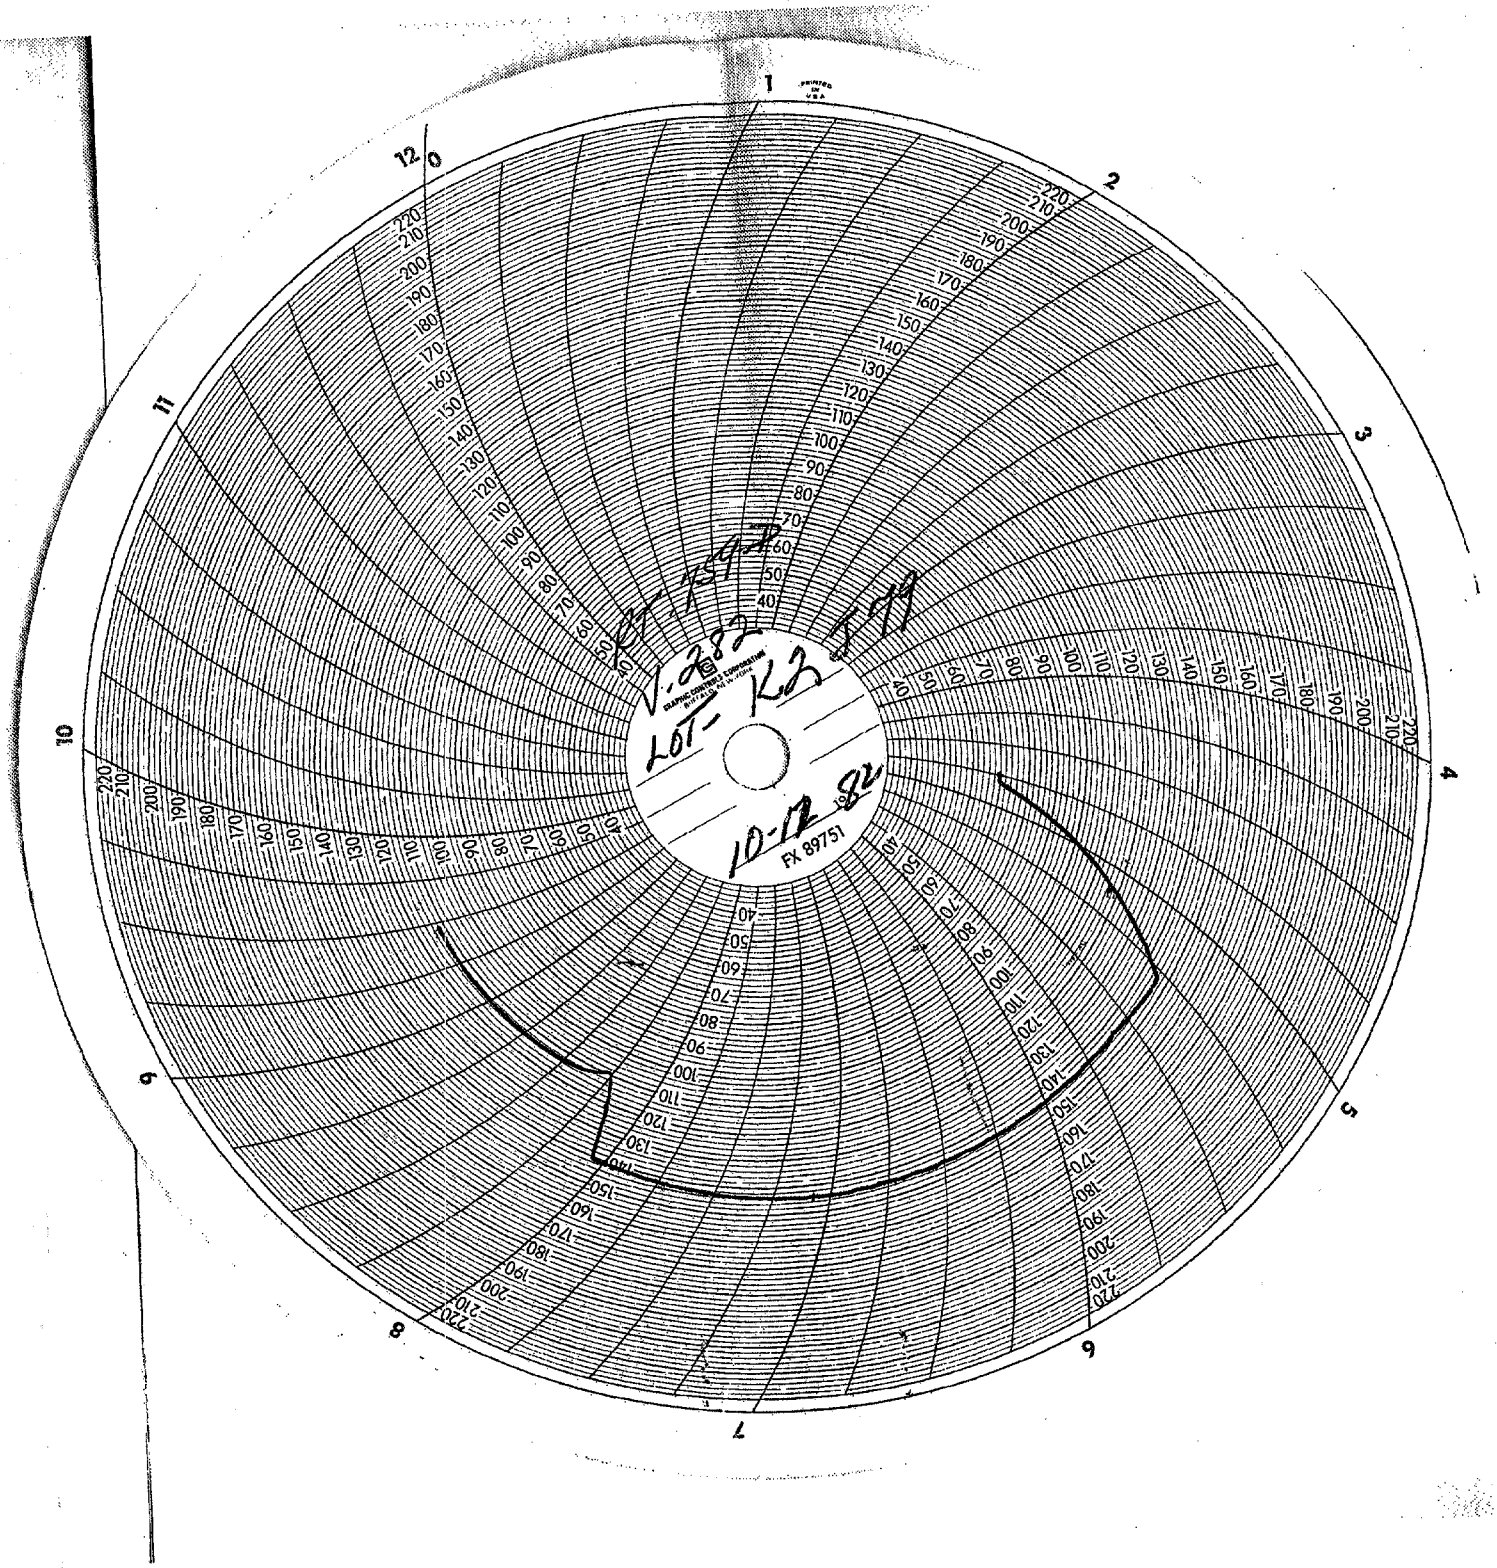


DUP050103515
