

Universal PFAS restriction Overall Timeline and Important Milestones

ECHA FFF restriction

Scope

Scope defined **for RoI** (exclusion WP2 and possible E-use WP7)

Scope defined **for Annex XV report** (ongoing assessments can still lead to changes in scope i.e. substances/substance groups to be excluded, uses to be derogated etc.)

2nd round CfE

Call for Evidence for specific information (15. July - 15. September)

Assessment of CfE info only for specific information requested (15. September -15. October)

Update of drafts of Annex A and Annex B specifically (15. October- End November)

Annex XV report Part 2 (Annexes)

Annex A. Manufacture and uses

Annex B. Information on hazard, exposure/emissions and risk

Phys-chem, Grouping

Information on hazards

Exposure/Emission

Risk

Annex C. Justification for action on a Union-wide basis

Annex D. Baseline

Annex E. Impact Assessment

Use and function of alternatives

Hazards of Alternatives

Monitorability, Practicability

Annex F. Assumptions, uncertainties and sensitivities

Annex G. Stakeholder information

Annex XV Report Part 1 (Summary)

1. Problem identified

1.1. Hazard, exposure/emissions and risk

1.2 Justification for an EU wide restriction measure

1.3. Baseline

2. Impact assessment

2.1. Introduction

2.2. Risk management options
2.3. Response to restriction scenario(s)
2.4. Economic impacts
2.5. Human health and environmental impacts
2.6. Other impacts
2.7. Practicability and monitorability
2.8. Proportionality to the risk (including comparison of options)
3. Assumptions, uncertainties and sensitivities
4. Conclusion
Finalisation of dossier for submission
Lay-out, text combining, proof-reading, final adjustments
Unexpected delay, dossier submission

Further
points
to consider

Endnote to be used as citation tool
Clarification of need of IUCLID dossier

Legend

WP0: blue
WP1: green
WP2: orange
WP3: yellow
WP4: grey
WP5: purple
WP6: -
WP7: red/brown

First draft = 70 % ready
Final draft = 90 % ready


WP responsible for keeping deadline	WP that need to deliver	First draft (70% version)	Final draft (90% version)	Final Deadline	May 21
-------------------------------------	-------------------------	---------------------------	---------------------------	-----------------------	--------



WP2 and WP7	WP3, WP4	7/15/2021	
	WP3, WP4, WP7	10/31/2021	

	WP4 sub uses	9/30/2021	11/30/2021	1/31/2022	
		11/30/2021	11/30/2021	4/15/2022	
	WP2	11/30/2021	11/30/2021	4/15/2022	
	WP6	11/30/2021	11/30/2021	4/15/2022	
	WP6, sub-WP4s	9/30/2021	11/30/2021	1/31/2022	
		11/30/2021	11/30/2021	4/15/2022	
	WP3, WP4, WP5	9/30/2021	11/30/2021	1/31/2022	
		9/30/2021	11/30/2021	1/31/2022	
		1/31/2022	3/31/2022	4/30/2022	
		9/30/2021	11/30/2021	1/31/2022	
		9/30/2021	11/30/2021	1/31/2022	
		9/30/2021	11/30/2021	1/31/2022	
		9/30/2021	11/30/2021	1/31/2022	
	WP4	1/31/2022	3/31/2022	4/30/2022	
	WP4 sub uses	9/30/2021	11/30/2021	1/31/2022	

	WP3, WP4 and WP6	4/30/2022
		3/31/2022
		3/31/2022
		4/30/2022



WP7

WP4

WP0


4/30/2022
4/30/2022
4/30/2022
4/30/2022
4/30/2022
4/30/2022
4/30/2022
4/30/2022
5/30/2022

WP0


WP0

6/30/2022
7/15/2022

Jun 21	Jul 21	15.07.21	Aug 21	Sep 21	Oct 21	Nov 21	Dec 21
--------	--------	----------	--------	--------	--------	--------	--------

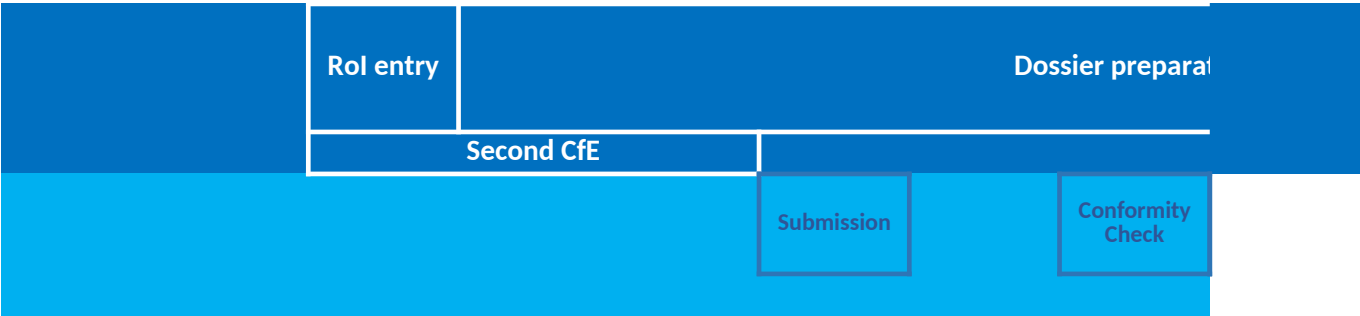

first draft	final draft	
	first draft	
	first draft	
	first draft	
first draft	final draft	
	first draft	
first draft	final draft	
first draft	final draft	
first draft	final draft	
first draft	final draft	
first draft	final draft	
	final draft	
first draft	final draft	





final



15.07.22

Submission
